
Business Requirements Document (BRD)

for

TaskFlow Q2/2025 — Work Management Platform

Version 1.0 – Draft

Prepared by Duy Thien

Personal Project

Date: April 2026

Table of Contents

1. Executive Summary	1
2. Business Objectives	1
2.1 Project Solution	1
2.2 Value.....	2
2.3 Next Steps.....	2
2.4 Functionality	3
2.5 Process Diagrams	3
3. Background	6
4. Scope.....	6
4.1 Project Objective	7
4.2 Project Deliverables.....	7
4.3 Project Milestones	7
4.4 High-Level Requirements.....	8
4.5 Assumptions	9
4.6 Acceptance Criteria	9
4.7 Constraints.....	10
5. Features.....	10
5.1 FT-007: Permission Module Refactor	10
5.2 FT-002: Time Tracking.....	11
5.3 FT-001: Export Excel/PDF.....	11
5.4 FT-006: Bulk Action	11
5.5 FT-003: Notification System	11
6. Functional Requirements	12
6.1 Context	12
6.2 Methodology.....	13
6.3 User Requirements	13
6.3.1 System Use Cases — Diagrams	13
6.3.2 System Use Case escriptions — FT-002: Time Tracking.....	15
6.3.3 System Use Case Descriptions — FT-001: Export Excel/PDF	16
6.3.4 System Use Case Descriptions — FT-006: Bulk Action	17
6.3.5 System Use Case Descriptions — FT-003: Notification System.....	17
6.4 User Requirements	18
6.5 Logical Data Model	19
7. Personnel Requirements.....	20
8. Reporting and Quality Assurance	20
9. Delivery Schedule.....	22
10. Other Requirements	22
11. Limitations.....	23
12. Risks	23
12.1 Technology Risks	24
12.2 Skills Risks	24
12.3 Environmental / Political Risks	25
12.4 Business Risks	25
12.5 Requirements Risks	26
12.6 Additional Risks	27
13. Appendix A — Glossary of Terms	27
14. Sign-off.....	28

Revision History

Name	Date	Reason For Changes	Version

1. Executive Summary

This section provides an overview of the document's purpose and contents. It should be read by all stakeholders before reviewing the detailed sections.

Attached is the Business Requirements Document covering the work required by TaskFlow for its Q2/2025 feature delivery. Sections include: Business Objectives, Background, Scope, Features, Functional Requirements, Personnel Requirements, Reporting and Quality Assurance, Delivery Schedule, Other Requirements, Limitations, and Risks.

One of the core issues faced by TaskFlow's customers — Vietnamese Agency and SME businesses — is the inability to track billable hours per client and generate structured project reports without relying on external tools (Toggl, Excel, Zalo). The goal of the Q2/2025 project is to allow TaskFlow to deliver five features that eliminate these external dependencies and position the product as a complete work management solution for its target segment.

By delivering Time Tracking, Export Excel/PDF, Notification System, Bulk Action, and Permission Refactoring within Q2, TaskFlow gets the benefit of its engineering team's focused capacity and the BA team's structured requirements framework to deliver measurable business impact: reducing churn from 5.2% to below 3%, and growing MRR by 25% (~600M VND/month).

2. Business Objectives

This section details what TaskFlow hopes to accomplish with the Q2 project, including business drivers, stakeholders involved, and how the project impacts the overall business strategy.

2.1 Project Solution

The Q2/2025 feature delivery will help TaskFlow accomplish its goal of becoming the definitive work management platform for Vietnamese Agency and SME businesses. The development team will oversee quality at each sprint to avoid issues during deployment. The primary solution is the introduction of built-in Time Tracking for hourly client billing, removing the customer dependency on Toggl and directly addressing the core revenue model of agency customers.

2.2 Value

Thanks to the Q2 delivery, TaskFlow can move further toward its goal of growing MRR to 600M VND/month (+25%) while reducing customer churn to below 3%. By doing so, TaskFlow puts itself in a position to demonstrate healthy growth metrics for its planned Series A investment round in Q4/2025.

2.3 Next Steps

The success of the Q2 delivery will impact TaskFlow positively by unlocking Enterprise upsell revenue from time-tracking-dependent agency customers, closing blocked sales pipeline deals (180M VND/year in held deals), and retaining at-risk accounts currently evaluating Monday.com and Asana. In addition, established metrics will gauge the impact of each feature release (see Section 8). By implementing the Q2 features, TaskFlow can accomplish the following business goals:

1. TaskFlow must have the ability to track and report billable hours per client and project (Time Tracking).
2. TaskFlow must have the ability to export structured project and workload reports to Excel and PDF format (Export).
3. TaskFlow must have the ability to deliver real-time task event notifications via in-app and email channels (Notification System).
4. TaskFlow must have the ability to allow Project Managers to apply status and assignment changes across multiple tasks simultaneously (Bulk Action).
5. TaskFlow must have the ability to enforce clean, scalable permission roles that support all new Q2 features without incurring bug overhead (Refactor).

Stakeholders involved in the project:

Name	Title	Department
Minh Khoa (SH-01)	CEO / Co-founder	Executive
Thu Hang (SH-02)	Head of Sales	Sales
Bao Trung (SH-03)	Tech Lead	Engineering


Name	Title	Department
Linh Phuong (SH-04)	Customer Success Manager	Customer Success
Duy Thien	Business Analyst	Product


TaskFlow decided to pursue Q2 delivery because of three compounding business drivers: (1) a 5.2% churn rate driven by missing features, (2) lost and blocked sales deals worth over 180M VND/year due to Export and Time Tracking gaps, and (3) Permission Module technical debt adding 30–40% overhead to every new feature. Business objectives follow the SMART formula — specific, measurable, actionable, realistic, and time-bound.

2.4 Functionality

The new functionality provided by the Q2 delivery will allow TaskFlow to accomplish its goals of churn reduction and MRR growth. Changes will include additions to the task management module (Time Tracking, Bulk Action), the reporting module (Export Excel/PDF), the notification subsystem (Notification System), and the internal permission architecture (Refactor). The Refactor will not introduce any user-visible changes but will reduce future delivery risk across all modules.

2.5 Process Diagrams

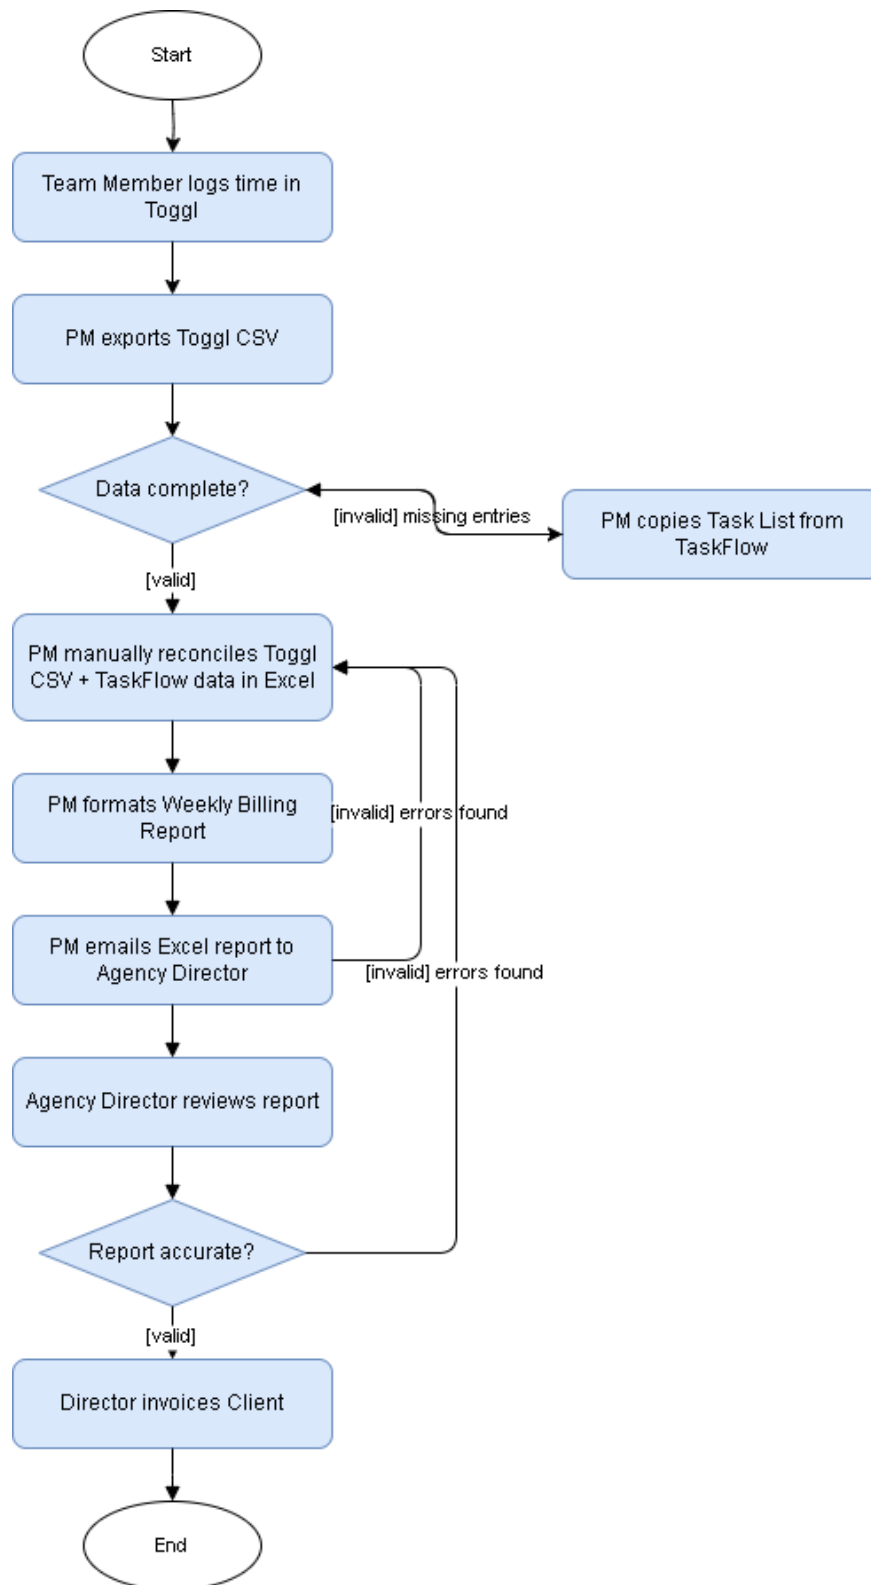Activity Diagram — Agency Time Billing: As-Is (Current State)

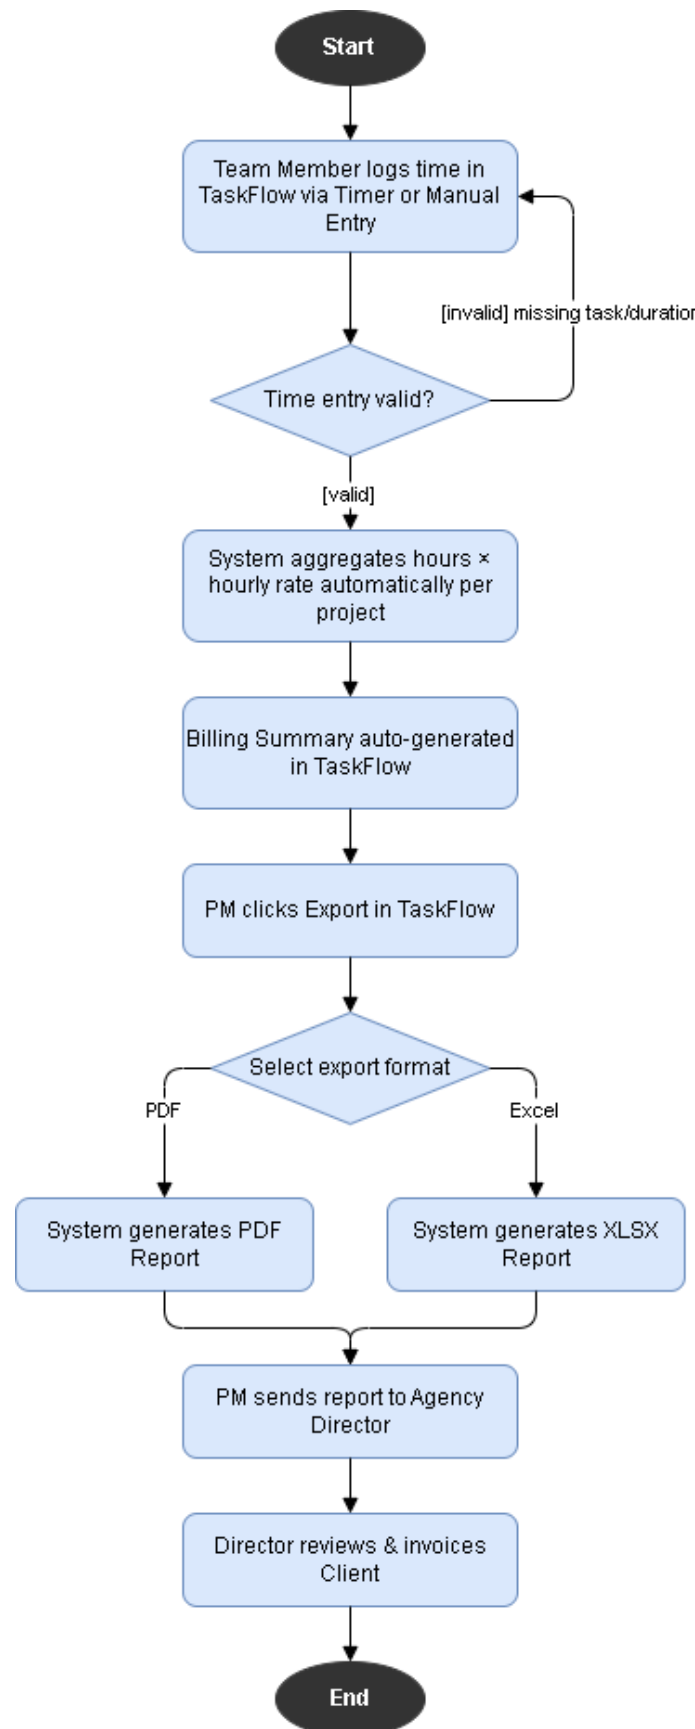Activity Diagram — Agency Time Billing: To-Be (Post Q2 Delivery)

3. Background

This section provides context about TaskFlow's current business practices and outlines the business need underlying this document.

Currently, TaskFlow's agency customers handle project billing and reporting by maintaining two parallel systems: TaskFlow for task management and Toggl for time tracking. Because of the increasing client base managed by Vietnamese agencies (typically 5–10 concurrent clients), the business must consolidate these workflows into a single tool. As a result, TaskFlow is initiating the Q2/2025 feature delivery to allow its engineering team to build the missing capabilities that agency and SME customers have explicitly identified as table-stakes for continued use and upgrade.

TaskFlow is the ideal partner to solve this problem because it is already embedded in the customer's project management workflow. Adding time tracking and reporting natively eliminates context-switching costs and data-entry errors inherent in multi-tool workflows. The platform's existing task, project, and permission structures provide a strong foundation on which Time Tracking and Export can be built efficiently.

Supporting background data: 89 support tickets received in Q1/2025 — the top three categories are Notification (18 tickets, 20.2%), Export Excel (14 tickets, 15.7%), and Mobile App (12 tickets, 13.5%). Six customers churned in Q4/2024–Q1/2025: four due to lack of Mobile App, one due to missing reporting, one due to pricing. Three current customers are actively evaluating competitors (Monday.com, Asana). Current MRR: 480M VND/month. Churn rate: 5.2% (board target: below 3%).

4. Scope

This section defines the boundaries of the Q2 project. Any services or project items not explicitly outlined within this section are deemed excluded from the project scope.

The scope of the Q2 project initiated by TaskFlow covers the following changes to business processes: the introduction of in-product time logging and billing summary to replace Toggl, structured data export to replace manual Excel compilation, real-time event notifications to replace Zalo-based status communication, multi-task editing to replace individual task update workflows, and internal permission architecture repair to enable all features to be built safely.

4.1 Project Objective

Prepared for: Minh Khoa — TaskFlow | **Prepared by:** Duy Thien (BA) | **Date:** 19/03/2025

The primary objective of the Q2 project is to deliver five features that address the two approved business objectives: reduce churn from 5.2% to below 3% (BO-1) and increase MRR from 480M to 600M VND/month (BO-2) by end of Q2/2025 (13 June 2025).

4.2 Project Deliverables

The deliverables within scope for the Q2 project include:

1. TaskFlow must provide customers with the ability to log, view, and export time spent on tasks per project — per team member and per client (Time Tracking — FT-002).
2. TaskFlow must provide Project Managers with the ability to export task lists, project progress summaries, and team workload data to Excel (.xlsx) and PDF formats (Export — FT-001).
3. TaskFlow must provide users with the ability to receive real-time in-app and email notifications for task assignment, overdue tasks, comments, and status changes (Notification System — FT-003).
4. TaskFlow must provide Project Managers with the ability to select multiple tasks simultaneously and apply status, assignee, or due date changes in a single action (Bulk Action — FT-006).
5. TaskFlow must provide its engineering team with a refactored Permission Module that supports five fixed roles (Owner, Admin, Project Manager, Member, Client) with a 30–40% reduction in permission-related bug overhead (Refactor — FT-007).

4.3 Project Milestones

#	Milestone	Target Date
4.3.1	BRD, Use Cases, and User Stories approved. Sprint 1 kickoff.	24/03/2025
4.3.2	FT-007 Refactor complete. All existing features regression-tested. Permission model documented.	07/04/2025

#	Milestone	Target Date
4.3.3	FT-002 Time Tracking beta released to 5 pilot customers. At least 1 Enterprise upgrade confirmed.	28/04/2025
4.3.4	FT-001 Export Excel/PDF (3 view types MVP) deployed. At least 2 blocked prospect deals re-opened.	19/05/2025
4.3.5	FT-006 Bulk Action and FT-003 Notification System deployed. Top support ticket categories resolved.	13/06/2025
4.3.6	UAT completed and signed off. Q2 close. Post-launch performance data collection begins.	13/06/2025

4.4 High-Level Requirements

The development team must adhere to each of the following high-level requirements:

ID	Requirement	Business Need
4.4.1	The system must allow Team Members to log time per task (manually or via timer).	Replace Toggl for in-product hourly billing (BO-2).
4.4.2	The system must aggregate logged hours per project per client with a configurable hourly rate.	Enable agency billable hours calculation (BO-2).
4.4.3	The system must export task, project, and workload data to .xlsx and .pdf formats.	Replace manual weekly Excel reporting (BO-1, BO-2).
4.4.4	The system must send in-app and email notifications upon task assignment, overdue status, comment addition, and status change.	Eliminate reliance on Zalo for task status updates (BO-1).
4.4.5	The system must allow multi-task selection and bulk application of status, assignee, and due date changes.	Reduce sprint-end PM workflow time (BO-1).
4.4.6	The Permission Module must support five roles (Owner, Admin, PM, Member, Client) without permission-related bugs carrying 30–40% overhead.	Enable reliable delivery of all Q2 features (BO-1 + BO-2 enabler).

ID	Requirement	Business Need
4.4.7	All features must enforce the role-based permission matrix defined in the Scope Document (Section 6).	Data isolation and access control compliance (CN-04).
4.4.8	All new features must be accessible via the existing TaskFlow web platform. No mobile-native implementation in Q2.	Constraint CN-03 — Mobile App is Q3 scope.

4.5 Assumptions

The development team should keep the following assumptions in mind when performing the Q2 work:

1. The team should assume that Export Excel MVP scope is confirmed as 3 view types only (Task List, Project Progress Summary, Team Workload). Full scope confirmation required from SH-02 and SH-04 by 17/03/2025 (Open Question Q-02).
2. The team should assume that the Refactor effort is fixed at 2 weeks, covering only the 5 fixed roles — no new permission logic is added in Sprint 1.
3. The team should assume that 4 developers are fully allocated to Q2 with no other parallel projects reducing capacity below 80% per sprint.
4. The team should assume that email/SMTP infrastructure is available within Sprint 1 budget with no additional procurement needed.
5. The team should assume that Time Tracking uses a single hourly rate per project (not per task or per role) for the MVP. This simplification has been validated as acceptable to Agency Director and PM personas.

4.6 Acceptance Criteria

1. The user must be able to start and stop a timer on any task they are assigned to, and have the duration recorded accurately in the time log.
2. The system must allow a Project Manager to export a Task List view for any project in both .xlsx and .pdf formats within 10 seconds of clicking "Export".
3. The user must be required to confirm bulk actions affecting more than 10 tasks before the system executes the change.

4. The system must validate that only users with the Owner or Admin role can view the client billing summary in Time Tracking before displaying the page.
5. The system must prompt the user to configure at least one notification preference before dismissing the notification setup prompt on first login following the feature release.
6. The system must deliver in-app and email notifications for task assignment events within 60 seconds of the assignment being saved.
7. The refactored Permission Module must pass 100% of the defined regression test cases before Sprint 2 begins.

4.7 Constraints

1. The current TaskFlow web application does not allow for mobile-native implementations. All Q2 features must work within the existing web platform.
2. Users of the TaskFlow system are currently limited to functions within the web browser. No desktop application or native mobile app is in Q2 scope.
3. The development team is constrained to a maximum of 4 developers over 11 weeks with no confirmed external contractor budget.
4. Reporting and billing data must remain isolated per agency account. Cross-account data access is explicitly prohibited by data isolation constraint CN-04.
5. Users can only process scheduled notifications via in-app and email channels in Q2 MVP. Zalo, Slack, and push notification channels are out of scope.

5. Features

This section introduces the features to be delivered upon completion of the Q2 project, describing business value and user capability for each.

TaskFlow will introduce the following features upon completion of the Q2 project:

5.1 FT-007: Permission Module Refactor

The development team must refactor the Permission Module in the TaskFlow system. The feature will give the engineering team the ability to build subsequent Q2 features (FT-002, FT-003, FT-

006) with 30–40% less time overhead and without incurring permission-related bugs. This is an internal technical feature — no user-visible changes. Delivered in Sprint 1.

5.2 FT-002: Time Tracking

The development team must add Time Tracking to the TaskFlow task management system. The feature will give the user the ability to log hours worked per task (via timer or manual entry), view aggregated hours per project, and allow Agency Owners and Admins to view client billing summaries showing billable hours multiplied by the project hourly rate. This replaces the current Toggl + manual reconciliation workflow.

5.3 FT-001: Export Excel/PDF

The development team must add Report Export to the TaskFlow project management system. The feature will give Project Managers and Owners the ability to export three structured report views — Task List, Project Progress Summary, and Team Workload — in both .xlsx and .pdf formats, enabling weekly client reporting without manual copy-paste workflows.

5.4 FT-006: Bulk Action

The development team must add Bulk Task Management to the TaskFlow task list. The feature will give the user the ability to select multiple tasks simultaneously via checkboxes and apply status changes, reassignment, due date updates, or deletion in a single action — reducing sprint-end status updates from 15–20 minutes to under 2 minutes.

5.5 FT-003: Notification System

The development team must add a Real-Time Notification System to TaskFlow. The feature will give Project Managers and Team Members the ability to receive immediate in-app alerts and email notifications when tasks are assigned, become overdue, receive comments, or change status — eliminating the current dependency on Zalo for task status communication.


6. Functional Requirements

This section provides detailed structural requirements for each feature. The audience includes both technical and non-technical decision-makers.


6.1 Context

The development team must provide TaskFlow with the following system updates, expanding functionality as outlined in the context diagrams below. These context diagrams show the system boundary and user interactions for Q2 features.

Context Diagram — Time Tracking Module (FT-002)

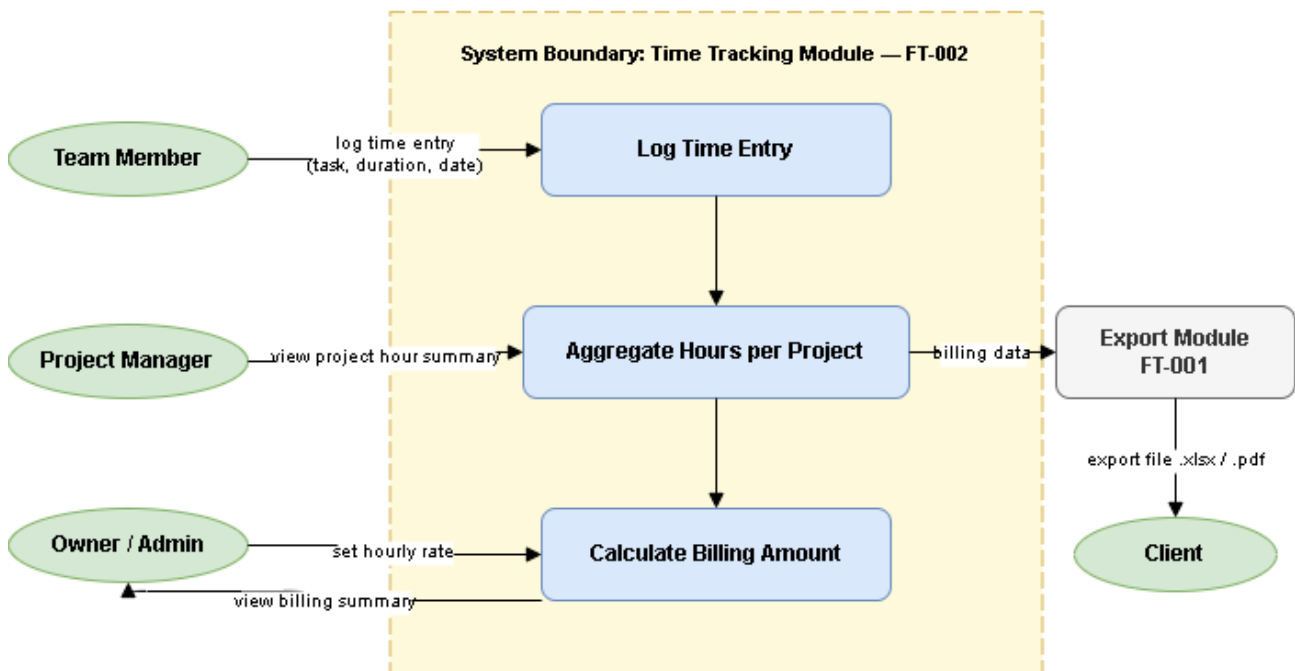

Context Diagram — Export & Notification Modules (FT-001, FT-003)

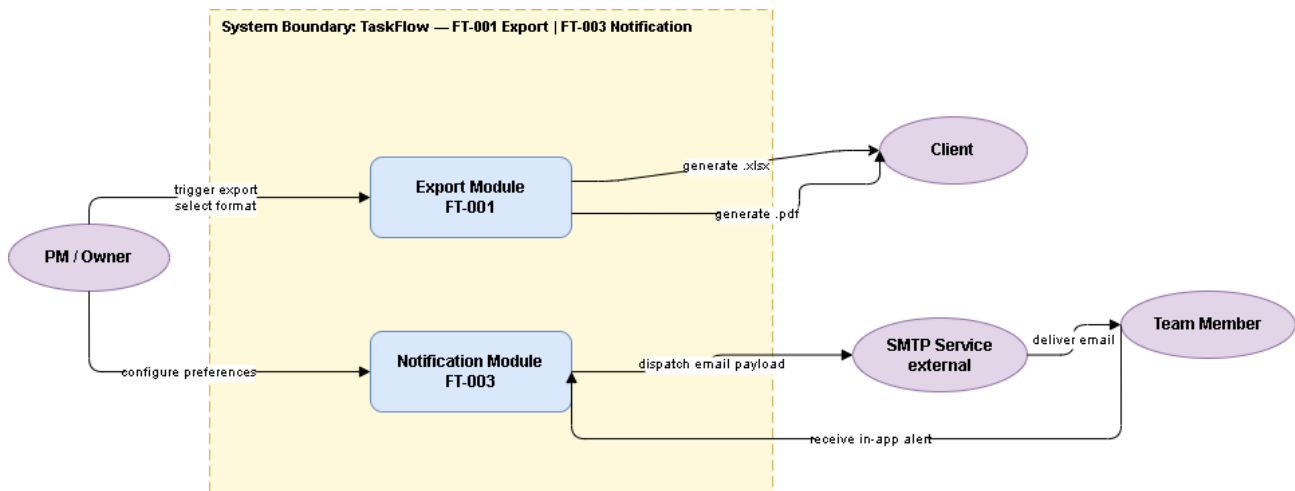

6.2 Methodology


The development team will adhere to an **Agile/Scrum** framework when planning out the different phases of the Q2 project. Sprint length is 2 weeks. This affords the development team and all project stakeholders the best chance of identifying potential risks to ensure they do not disrupt delivery. Sprint planning, sprint review, and retrospective ceremonies are maintained throughout Q2.

6.3 User Requirements

6.3.1 System Use Cases — Diagrams


The following diagrams provide a visualisation of what TaskFlow requires from the system:

Use Case Diagram — Time Tracking (FT-002)

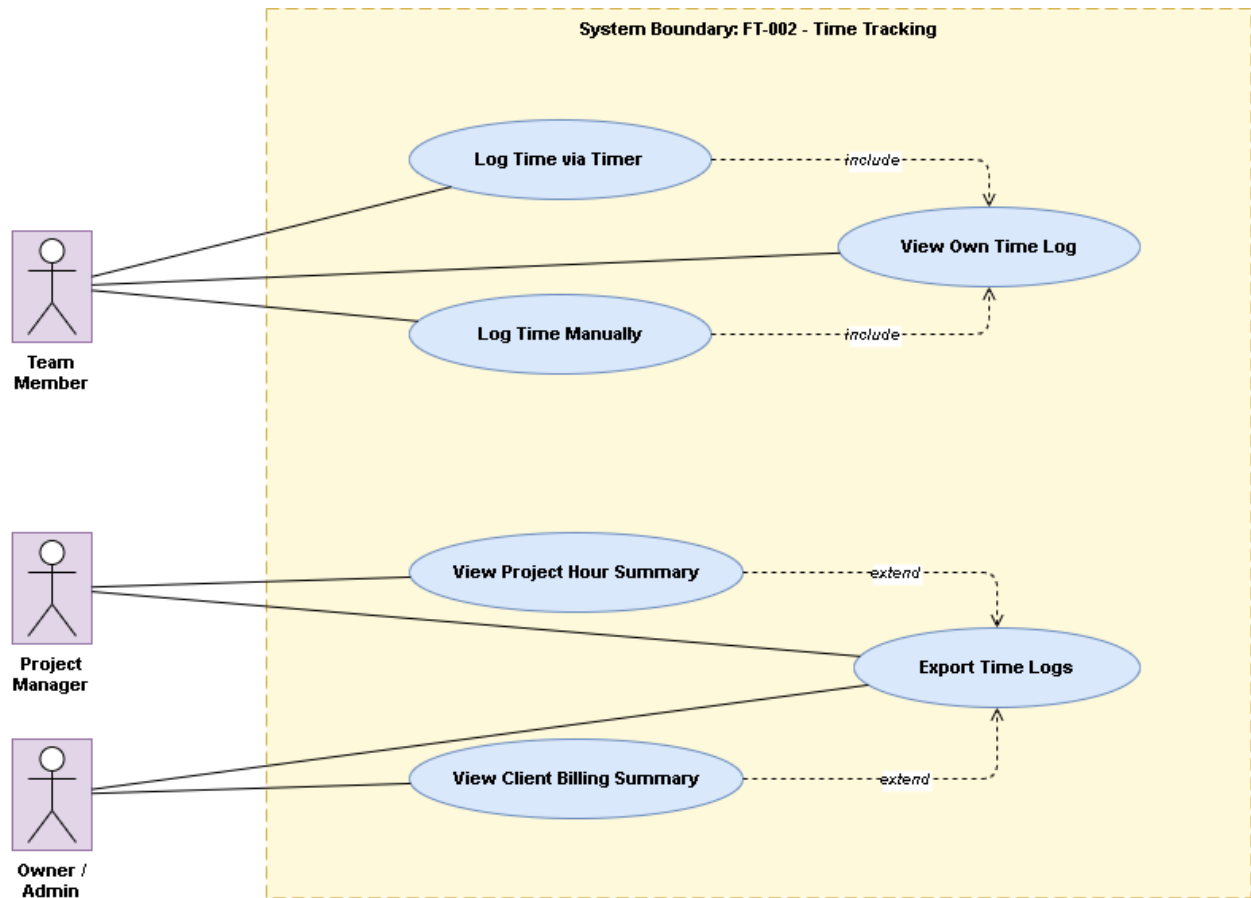

include = mandatory sub-flow | extend = optional extension

Use Case Diagram — Export (FT-001), Bulk Action (FT-006), Notification (FT-003)

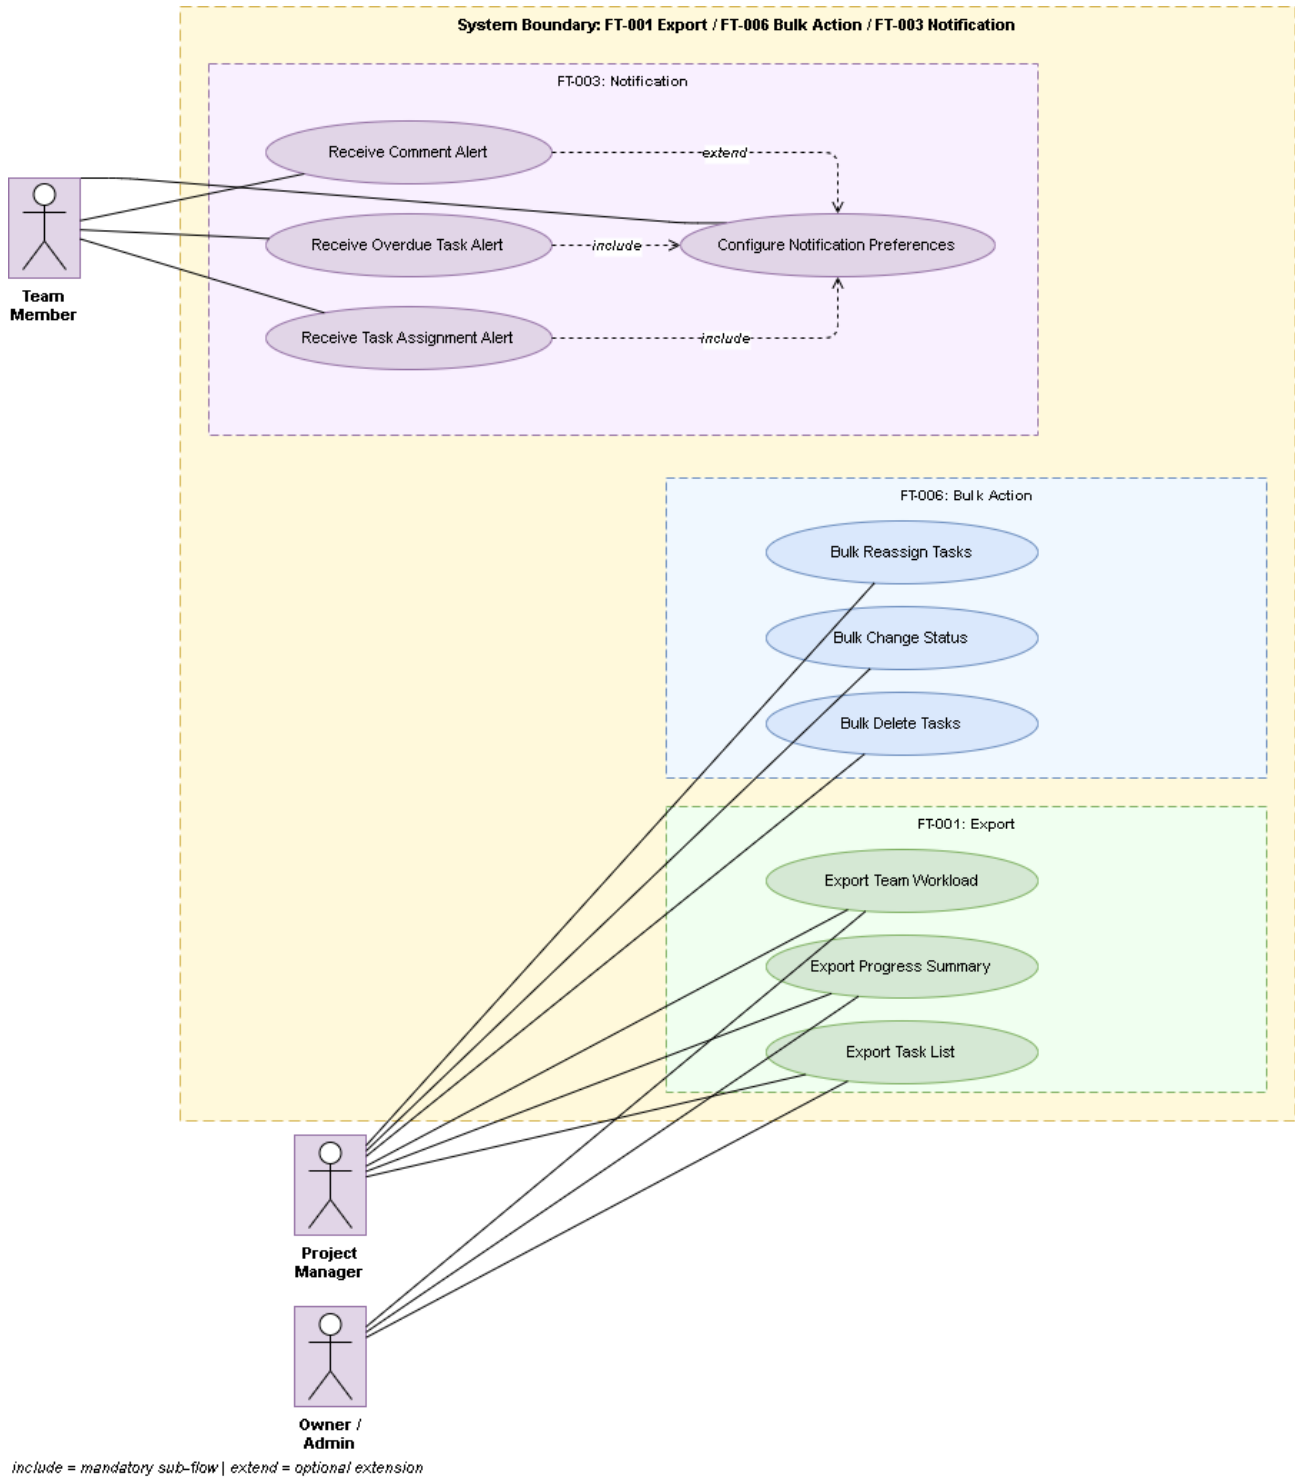

6.3.2 System Use Case descriptions — FT-002: Time Tracking

ID	Use Case	Actor	Pre-condition	Main Flow	Post-condition
UC-001	Log Time via Timer	Team Member	User is assigned to the task. Task is in status "In Progress".	1. User opens task detail. 2. Clicks Start Timer. 3. Works. 4. Clicks Stop Timer. 5. System records duration and saves log entry with date and user.	Time log entry created. Total hours for task updated.
UC-002	Log Time Manually	Team Member	User is assigned to the task.	1. User opens task detail. 2. Clicks Add Time. 3. Enters date, hours, and optional note. 4. Saves. 5. System records entry.	Time log entry created with manually entered duration.
UC-003	View Project Time Summary	Project Manager	User has PM role or above on the project. At least one time log exists.	1. PM navigates to Project Settings → Time Summary. 2. System displays table: team member vs. total hours logged.	PM sees aggregated hours per member for the project.
UC-004	View Client Billing Summary	Owner / Admin	User has Owner or Admin role. Hourly rate has been set for the project.	1. Owner navigates to Project → Billing Summary. 2. System calculates total hours × hourly rate. 3. Displays billable amount per client per period.	Owner sees billing summary ready for client invoice.

6.3.3 System Use Case Descriptions — FT-001: Export Excel/PDF

ID	Use Case	Actor	Main Flow	Post-condition
UC-005	Export Task List	PM / Owner	1. User clicks Export in project menu. 2. Selects View Type 1 (Task List). 3. Selects date range. 4. Selects format (.xlsx or .pdf). 5. Clicks Download. 6. System generates file	File downloaded. Contains task name, assignee, status, due date, priority columns.

ID	Use Case	Actor	Main Flow	Post-condition
			and triggers download.	
UC-006	Export Project Progress Summary	PM / Owner	1. Same trigger. 2. Selects View Type 2. 3. System generates single-page PDF: % completion, on-track flag, open blockers list.	Client-shareable PDF downloaded.
UC-007	Export Team Workload	PM / Owner	1. Same trigger. 2. Selects View Type 3. 3. System generates .xlsx: tasks grouped by assignee, hours logged per assignee (if FT-002 active).	.xlsx file downloaded with workload data by team member.

6.3.4 System Use Case Descriptions — FT-006: Bulk Action


ID	Use Case	Actor	Main Flow	Post-condition
UC-008	Bulk Change Task Status	PM / Owner	1. PM checks multiple task checkboxes in Task List view. 2. Floating action bar appears. 3. PM selects "Change Status". 4. Selects new status from dropdown. 5. System shows confirmation: "Change status for [N] tasks?" 6. PM confirms. 7. System applies change to all selected tasks.	All selected tasks updated to new status. Audit log entry created per task.
UC-009	Bulk Reassign Tasks	PM / Owner	1. Select tasks. 2. Choose "Reassign". 3. Select new assignee. 4. Confirm. 5. System reassigns all selected tasks and triggers assignment notification (FT-003) for the new assignee.	Tasks reassigned. Notifications sent.
UC-010	Bulk Delete Tasks	PM / Owner	1. Select tasks. 2. Choose "Delete". 3. System shows warning: "This action cannot be undone. Delete [N] tasks?" 4. User types "DELETE" to confirm. 5. System permanently deletes tasks.	Tasks deleted. Action logged.

6.3.5 System Use Case Descriptions — FT-003: Notification System


ID	Use Case	Actor	Trigger	System Action
UC-011	Receive Task Assignment Notification	Team Member	PM assigns task to Team Member.	System sends in-app notification + email to assignee within 60 seconds. Notification shows: task name, project name, assigned by, link to task.
UC-012	Receive Overdue Task Alert	PM	Task due date passes and status is not "Done".	System sends in-app notification + email to task assignee and PM. Alert includes: task name, days overdue, project link.
UC-013	Receive Comment Notification	Task Assignee	Any project member adds a comment on a task the user is assigned to or watching.	System sends in-app notification + email with commenter name, comment excerpt (first 100 chars), and link to task.
UC-014	Configure Notification Preferences	Any User	User navigates to Settings → Notifications.	System displays preference table: trigger types as rows (Assigned, Overdue, Comment, Status Change), channels as columns (In-App, Email). User toggles ON/OFF per cell. System saves preferences immediately.

6.4 User Requirements

DATA FLOW DIAGRAM — TIME TRACKING (FT-002)

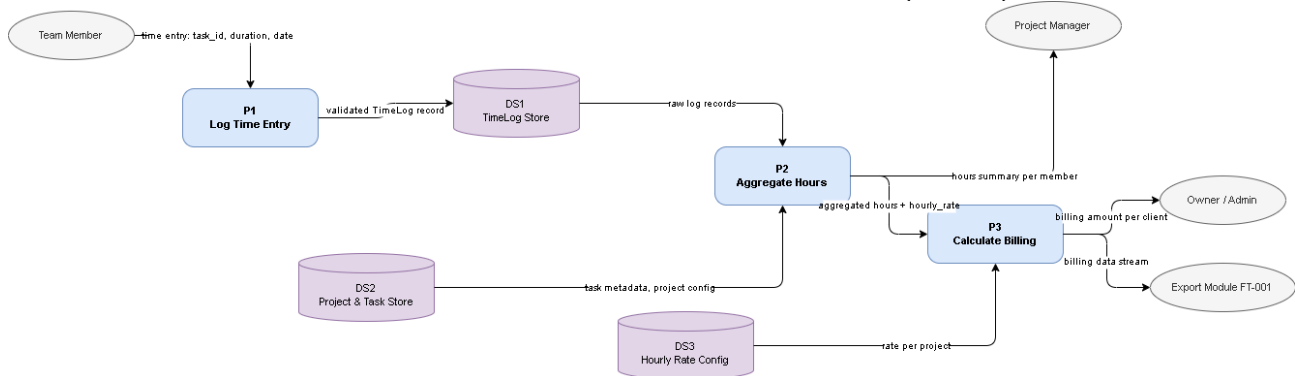


DATA FLOW DIAGRAM — NOTIFICATION SYSTEM (FT-003)

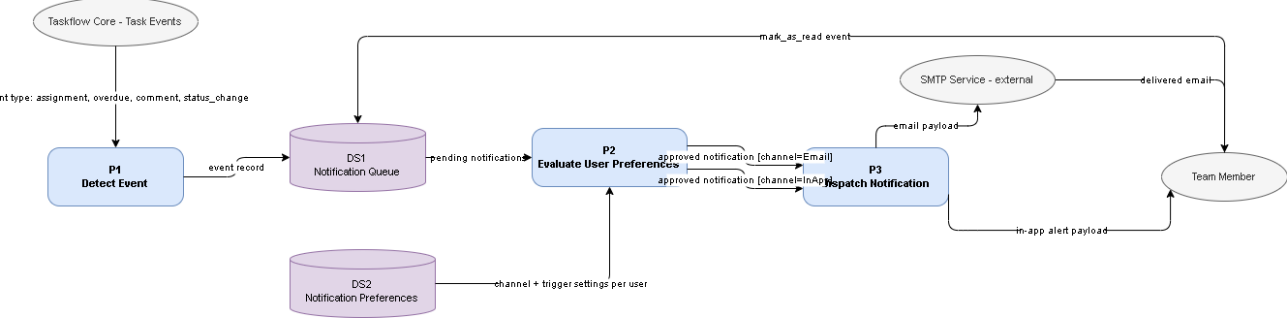

6.5 Logical Data Model

Logical Data Model — Q2 Features Entities & Relationships

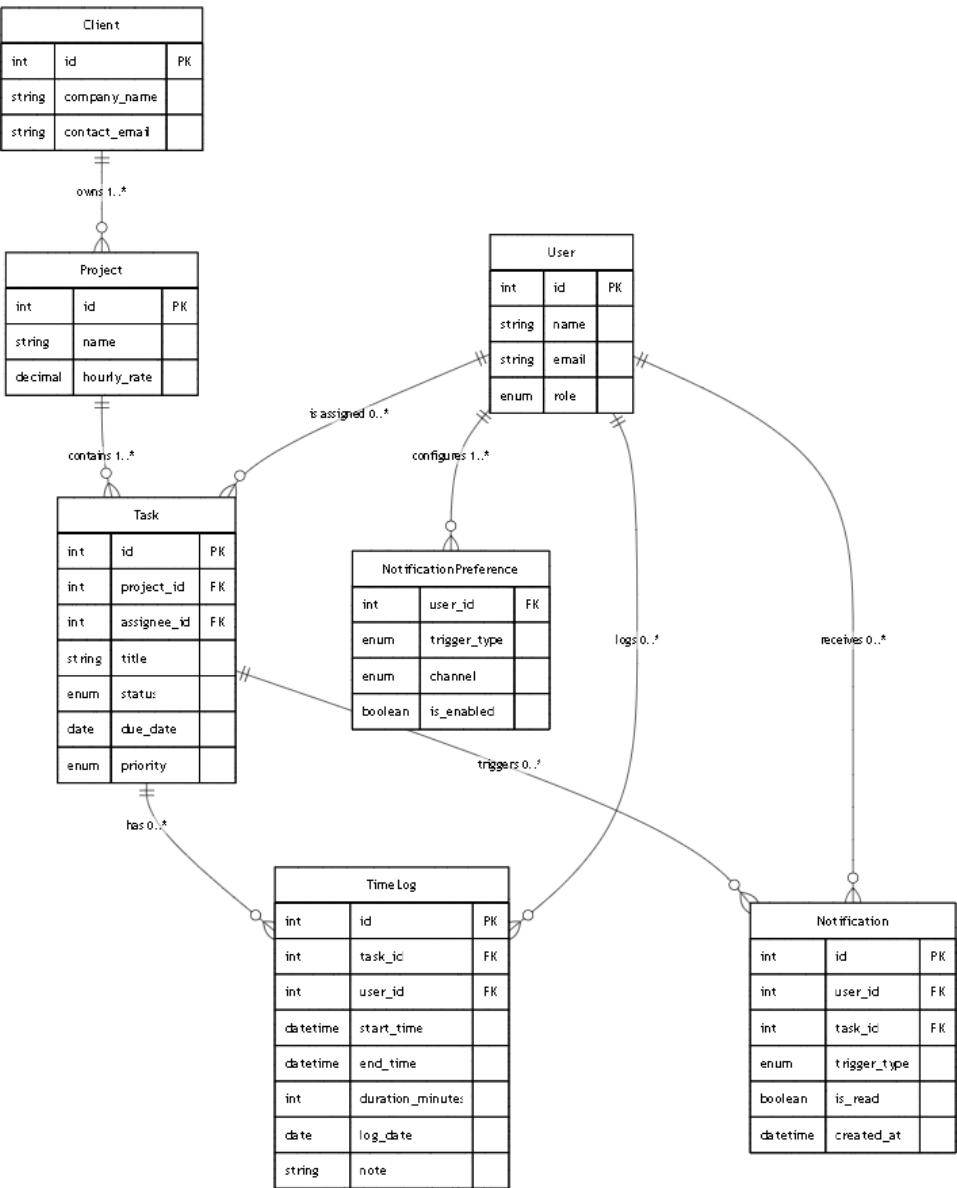

7. Personnel Requirements

This section outlines the personnel required to ensure the timely completion of the Q2 project.

Role	Skills	Estimated Hours (Q2)	Cost / Week
Business Analyst — Duy Thien	Requirements elicitation, BRD/SRS writing, use case modelling, wireframe briefing, UAT facilitation	376 hrs (47 days)	Salaried — internal
Tech Lead / Senior Developer (×2)	Full-stack development, system architecture, permission module refactor, code review	880 hrs combined (11 wks × 2 × 40 hrs)	3.5M VND/person/week
Junior Developer (×2)	Frontend implementation, API integration, unit testing, bug fixing	880 hrs combined	2.1M VND/person/week
Product Designer (TBD)	Wireframe and mockup design (Stitch MCP), UI component specification, design review	~80 hrs (Wk 4–7)	TBD — pending Q-04 (external budget)
QA Engineer (TBD)	Test case execution, regression testing, UAT coordination	~80 hrs (Wk 9–11)	TBD
Customer Success Manager — Linh Phuong	Pilot customer recruitment, UAT facilitation, post-launch adoption monitoring	~40 hrs (support role)	Salaried — internal

Note: Designer and QA are flagged as TBD pending CEO (SH-01) resolution of Open Question Q-04 (external contractor budget). If not engaged, BA and Tech Lead absorb these roles at reduced quality assurance coverage.

8. Reporting and Quality Assurance

This section outlines how progress is measured and assessed. Metrics must be clearly defined to show progress to stakeholders throughout Q2.

Metric ID	Metric Name	Measurement Method	Target	Review Cadence
QA-01	Churn Rate	Monthly churn rate from customer database (cancellations / active at start of month)	<3% by end of Q2	Monthly
QA-02	MRR Growth	Total Monthly Recurring Revenue extracted from billing system	600M VND/month by end of June 2025	Monthly
QA-03	Time Tracking Adoption Rate	% of active customers that have logged at least 1 time entry within 30 days of feature release	>60% of active customers within 30 days	30 days post-release
QA-04	Export Feature Usage	Number of export downloads per week from product analytics	>50 exports/week within 4 weeks of release	Weekly (post-release)
QA-05	Support Ticket Volume Reduction	Count of tickets in top 3 categories (Notification, Export, Bulk Action) per month	Reduce from 43 tickets/month to <15 tickets/month	Monthly
QA-06	Permission Bug Rate	Number of bugs filed against permission-related functionality per sprint (post-refactor)	0 critical permission bugs per sprint in Q2 after Sprint 1	Per sprint
QA-07	NPS Score	Net Promoter Score from quarterly customer survey (CSM administers)	NPS >40 by end of Q2 (currently 32)	Quarterly
QA-08	Sprint Velocity (Dev)	Story points delivered per sprint vs. committed story points	>85% sprint commitment achieved across Q2	Per sprint

9. Delivery Schedule

This section includes final deadlines and milestones for each project phase. The development team must adhere to the delivery schedule.

Phase	Deliverable	Deadline
9.1 Planning	The development team must deliver signed BRD, Use Cases, User Stories, and approved BA Delivery Plan by 24 March 2025.	24/03/2025
9.2 Sprint 1	The development team must deliver FT-007 (Permission Refactor) — complete, regression-tested, documented — by 7 April 2025.	07/04/2025
9.3 Sprint 2–3	The development team must deliver FT-002 (Time Tracking) beta — timer, manual log, project summary, billing summary — by 28 April 2025.	28/04/2025
9.4 Sprint 3–4	The development team must deliver FT-001 (Export Excel/PDF — 3 view types MVP) by 19 May 2025.	19/05/2025
9.5 Sprint 5	The development team must deliver FT-006 (Bulk Action — status, reassign, date, delete with confirm) by 2 June 2025.	02/06/2025
9.6 Sprint 5–6	The development team must deliver FT-003 (Notification System — in-app + email, 4 trigger types, preference panel) by 13 June 2025.	13/06/2025

10. Other Requirements

This section covers interface, infrastructure, and non-functional requirements not addressed in other sections.

1. The development team must provide TaskFlow with the ability to process time log entries with a round-trip response time of under 2 seconds for save operations.
2. The development team must provide TaskFlow with the ability to generate and download Export files (Excel/PDF) within 10 seconds for project datasets of up to 1,000 tasks.
3. The development team must provide TaskFlow with the ability to dispatch Notification events to the notification queue within 10 seconds of the triggering action being saved in the database.

4. The development team must provide TaskFlow with the ability to deliver email notifications via an SMTP or transactional email service (e.g., SendGrid, AWS SES) — infrastructure selection is at Tech Lead discretion.
5. The development team must provide TaskFlow with the ability to persist all time log entries with full audit history (entry creation, edits, deletions) — supporting future billing dispute resolution.

11. Limitations

This section identifies limitations that may impact delivery. Capturing these upfront reduces the potential for the project to be derailed by unanticipated challenges.

1. The current TaskFlow web platform prevents the development team from delivering mobile push notifications in Q2, as no native mobile app exists. In-app and email are the only available notification channels.
2. Current company resource policy limits the dev team to 4 internal developers, which prevents parallel development of Mobile App and the 5 in-scope Q2 features simultaneously.
3. A lack of a dedicated QA engineer limits the ability of the BA and Tech Lead to perform full independent test coverage beyond unit and integration tests in Q2.
4. A need to comply with data isolation requirements (CN-04) prohibits any shared data view across competing agency accounts, requiring per-account data scoping to be enforced at the database query level — which adds complexity to the Time Tracking billing module.
5. The Export feature's data export is limited to 3 view types in Q2 MVP. The remaining 9 view types (Gantt, Budget, Time Billing Report, etc.) must be deferred, limiting the breadth of reporting immediately after launch.

12. Risks

Every project has inherent risks. This section identifies them and outlines mitigation approaches. Stakeholder brainstorming was conducted during the meeting of 14/03/2025 to identify all risks.

12.1 Technology Risks

ID	Risk	Impact	Mitigation
TR-01	If the Permission Module Refactor uncovers deeper architectural issues than estimated, the development team will not be able to complete Sprint 1 within 2 weeks, delaying all downstream features.	High — cascades into all 4 dependent features	Tech Lead (SH-03) conducts a 1-day refactor discovery session before Sprint 1 kicks off. Scope is hard-capped at the 5 fixed roles only. Any additional architectural work is a scope change requiring SH-01 approval.
TR-02	If the email infrastructure does not support the notification event volume (estimated 500+ notifications/day at current customer scale), the system will not deliver notifications within the 60-second SLA.	Medium — degrades FT-003 feature quality	Tech Lead selects transactional email service (SendGrid/SES) with rate capacity above 10,000 emails/day before Sprint 5. Load test notification queue before production release.
TR-03	If the data storage does not properly save time log entries when concurrent users submit logs simultaneously, that will affect the integrity of billing data in the Time Tracking module.	High — billing errors damage customer trust	Implement database-level locking on time log inserts. Unit test concurrent write scenarios before beta release. SH-04 (CSM) monitors pilot customer reports during beta period.

12.2 Skills Risks

The following risks might arise due to personnel capabilities:

ID	Risk	Mitigation
SR-01	If the junior developers do not possess sufficient knowledge of the PDF generation library required for FT-001, they will not be capable of producing correctly formatted PDF exports within the Sprint 3–4 estimate.	Tech Lead assigns PDF export task to a Senior Developer. Junior developers handle .xlsx export (lower complexity). Tech Lead conducts a tech spike on PDF library options in Week 2.
SR-	If users (Agency PMs and Members) do not	CSM (SH-04) prepares a 2-page onboarding

ID	Risk	Mitigation
02	understand how to use the Time Tracking tab upon feature release, they will not adopt the feature, defeating the MRR growth objective.	guide and conducts a 30-minute live walkthrough with the 5 pilot customers during the beta period. In-app tooltip hints are included in the UI spec.

12.3 Environmental / Political Risks

ID	Risk	Mitigation
EP-01	If the Head of Sales (SH-02) is unable to obtain buy-in from Agency Director prospects on the Export Excel MVP (3 view types only), that impacts TaskFlow's ability to close the blocked deals attributed to this feature in the Business Case ROI model.	BA documents Export MVP scope decision and rationale in writing. SH-02 communicates the Q3 roadmap for remaining view types to prospects during sales conversations.
EP-02	If Vietnamese data protection regulations evolve to require explicit user consent for email notification sending during Q2, TaskFlow will be unable to send email notifications without a consent flow, delaying FT-003 delivery.	BA monitors regulatory landscape with SH-01. Email opt-out mechanism is included in FT-003 design by default, providing a baseline compliance posture.

12.4 Business Risks

ID	Risk	Mitigation
BR-01	If Open Question Q-02 (Export scope: 3 vs. 12 views) is not resolved by 17/03/2025, the BA will not be able to finalise FT-001 requirements, blocking the Sprint 3–4 start and compressing the delivery schedule.	BA escalates to SH-01 on 17/03 if unresolved. CEO makes binding scope decision. BA documents and proceeds.
BR-02	If stakeholders fail to provide timely review and sign-off on the BRD within 5 business days, the	All review sessions are scheduled at least 5 days in advance. Async written review is

ID	Risk	Mitigation
	sprint kickoff will be delayed and Q2 delivery dates will shift.	accepted as an alternative to live sessions. SH-01 has final authority to approve in case of disagreement.
BR-03	If the 5 pilot customers recruited for Time Tracking beta decline to participate or do not actively use the feature during beta, the feature will launch without validated real-world usage data, increasing post-launch adoption risk.	SH-04 (CSM) recruits pilot customers by Wk 2 with an incentive communicated (e.g., early access, priority support). Minimum 3 active pilot users required before general release is approved.

12.5 Requirements Risks

ID	Risk	Mitigation
RR-01	If the BA and development team fail to account for all user roles affected by new permissions in FT-002, FT-003, and FT-006, that may impact the ability to deliver complete and secure features that pass UAT.	The Role Permission Matrix in Scope Document Section 6 is used as a mandatory checklist for every feature's BRD section. All 5 roles must be covered before a requirement is marked complete.
RR-02	If the BA and development team fail to account for edge cases in Time Tracking (e.g., overlapping timers, zero-duration entries, timer running across midnight), that may cause data integrity issues in the billing summary module.	BA documents edge case handling rules in the User Stories acceptance criteria (DOC-07). Tech Lead reviews edge cases during Sprint 2 planning before coding begins.
RR-03	If the BA and development team fail to account for all user notification preferences (users who want zero email notifications), that may result in unwanted email volume and customer complaints following FT-003 launch.	FT-003 includes a mandatory opt-out mechanism per trigger type per channel. Default state for email notifications is OFF — users must actively opt-in.

12.6 Additional Risks

ID	Risk	Mitigation
AR-01	The potential of a competitor (Monday.com, Asana) releasing a Vietnamese-language version or a significant price reduction during Q2 could impact TaskFlow's ability to retain the 3 at-risk accounts identified by SH-04.	CSM (SH-04) proactively schedules Quarterly Business Reviews with all 3 at-risk accounts during Q2. BA ensures FT-001 and FT-002 delivery is communicated to these accounts as a concrete Q2 commitment.
AR-02	The potential of a key developer resigning during the project development phase could impact TaskFlow's ability to deliver on Sprint 2–3 milestones (Time Tracking — the highest-complexity feature).	Tech Lead maintains internal documentation and code comments throughout Q2. No single-point-of-knowledge development is permitted. BA maintains requirements artefacts that can onboard a replacement.

13. Appendix A — Glossary of Terms

Term	Definition
BRD	Business Requirements Document — a formal document that describes the scope, features, functional requirements, and delivery plan for a project from a business perspective.
MRR	Monthly Recurring Revenue — the predictable total revenue generated by all active subscriptions in a given month.
Churn Rate	The percentage of customers who cancel their subscription within a given month. Formula: $(\text{Cancellations} / \text{Active customers at start of month}) \times 100$.
Time Tracking	The process of recording the amount of time a team member spends on a specific task. Used by agencies to calculate client billing amounts.
Billing Summary	A report showing the total billable hours per client per billing period, multiplied by the configured hourly rate. Used by Agency Owners to prepare client invoices.
Permission Module	The internal software component in TaskFlow responsible for enforcing role-based access control — determining which users can view, edit, or delete specific data.

Term	Definition
Refactor	The process of restructuring existing code without changing its external behaviour, to improve maintainability, reduce bugs, and accelerate future development.
SMART Goals	Goals that are Specific, Measurable, Actionable, Realistic, and Time-bound.
UAT	User Acceptance Testing — the final phase of testing where end users verify that the system meets their requirements before it is released to production.
Use Case	A description of how a specific type of user interacts with a system to achieve a particular goal, including the main flow and any alternative flows.
Sprint	A fixed-length development cycle (2 weeks in this project) during which the development team commits to delivering a defined set of features or tasks.
SMTP	Simple Mail Transfer Protocol — the standard communication protocol used for sending emails between servers.
NPS	Net Promoter Score — a customer loyalty metric calculated from the question "How likely are you to recommend this product to a friend?" on a 0–10 scale.
Tech Debt	The accumulated cost of shortcuts or suboptimal design decisions made during earlier development, which must eventually be paid through refactoring or rework.

14. Sign-off

By signing below, stakeholders confirm that this BRD accurately represents the Q2/2025 business requirements and authorise the BA to proceed to Use Cases (DOC-06) and User Stories (DOC-07).

Role	Name	Date Reviewed	Decision (Approve / Reject / Revise)
CEO / Co-founder	Minh Khoa (SH-01)		
Head of Sales	Thu Hang (SH-02)		

Role		Name	Date Reviewed	Decision (Approve / Reject / Revise)
Tech Lead		Bao Trung (SH-03)		
Customer Manager	Success	Linh Phuong (SH-04)		
