
Business Case: Q2/2025 Feature Delivery Strategy

for

TaskFlow — Work Management Platform

Version 1.0 - Draft

Prepared by Duy Thien

Personal Project

Date: Apr 2026

Table of Contents

- 1. Executive Summary1
- 2. Problem Statement & Opportunity1
 - 2.1 Current State..... 2
 - 2.2 Desired State 2
 - 2.3 Gap..... 2
 - 2.4 Cost of Inaction (Do Nothing — Option A)..... 2
- 3. Options Analysis.....3
 - 3.1 Options Summary 3
- 4. Cost Analysis — Option C (Recommended)4
 - 4.1 One-Time Development Costs 4
 - 4.2 Deferred Items (Not in Q2 Budget) 4
- 5. Benefit Analysis — Option C4
 - 5.1 Quantifiable Benefits 5
 - 5.2 Non-Quantifiable Benefits 5
- 6. Financial Summary5
 - 6.1 Monthly Cash Flow Projection..... 6
- 7. Risk Assessment6
 - 7.1 Sensitivity Analysis 7
- 8. Implementation Plan8
- 9. Recommendation8
 - 9.1 Assumptions & Limitations 9
- 10. Sign-off.....9

Revision History

Name	Date	Reason For Changes	Version

1. Executive Summary

This section provides decision-makers with a concise summary of the recommendation and the financial outcome of the recommended option. Full analysis follows in Sections 3–8.

Recommendation: APPROVE Option C — Foundation-First Delivery

Decision	Approve Option C: Refactor Permission Module (Sprint 1) → Time Tracking → Export Excel → Bulk Action → Notification System (Sprints 2–6).
Investment Required (Q2)	~112M VND (10 weeks of 4-developer team at blended rate 2.8M VND/dev/week)
Expected MRR Increase (12-month)	+108M to +132M VND/month from Time Tracking upsell (4 prospects × 8–10M VND/month) + Export Excel (1 renewal secured + 5 prospect deals)
Churn Reduction Value (12-month)	~24M VND/month recovered by reducing churn from 5.2% to <3% (approx. 2.4 accounts retained/month × 10.2M VND avg. account MRR)
Estimated Payback Period	4–5 months post-delivery
Risk Level	Low to Medium — mitigated by refactoring first, which reduces delivery risk for all subsequent features by 30–40%.
Decision Needed By	18 March 2025 (to begin Sprint 1 on 24 March)
Approval Authority	SH-01 Minh Khoa (CEO)

2. Problem Statement & Opportunity

This section articulates the current state problem, the desired state after Q2, and the cost of inaction if no feature delivery decision is made.

2.1 Current State

TaskFlow has 47 active customers with a churn rate of 5.2% (Q1 2025). The product backlog contains 60+ unresolved feature requests. Customers are using TaskFlow alongside parallel tools — Zalo for notifications, Toggl for time tracking, Excel for client reporting — indicating that the product is not yet a complete solution for its target segment (Vietnamese Agency & SME). Two deals worth a combined ~180M VND/year were lost in March 2025 alone due to the absence of Export Excel functionality.

2.2 Desired State

By end of Q2 2025, TaskFlow should deliver the two highest-impact features (Time Tracking, Export Excel) to: (a) convert 4 identified prospects to paid accounts, (b) retain at-risk existing customers, and (c) position the platform as the definitive work management tool for Vietnamese agencies who bill clients by the hour.

2.3 Gap

The current product lacks at least two table-stakes features for the agency segment: built-in time tracking for client billing, and structured Excel/PDF report export for weekly client reporting. Additionally, the Permission Module technical debt causes a 30–40% overhead on every new feature, making Q2 delivery targets unachievable without first addressing this internal blocker.

2.4 Cost of Inaction (Do Nothing — Option A)

Risk Category	Quantified Impact	Source
Lost new deals (Export Excel)	180M VND/year minimum (1 confirmed deal). Further deals at risk: 5 prospects value ~180M VND/year total pipeline.	Head of Sales (SH-02) — 14/03/2025
Missed Time Tracking upsell	4 prospects ready to convert to Enterprise plan: estimated +32M to +40M VND/month MRR uplift.	Customer Feedback Email 05; SH-02
Continued churn	At current 5.2% rate: ~2.4 accounts lost per month × 10.2M VND avg. = ~24.5M VND MRR lost per month.	CSM Data (SH-04); BA calculation
Accelerating tech debt cost	Each feature built without refactor costs 30–40% additional engineering time. Over 5 features in Q2, this adds ~4 weeks of waste.	Tech Lead (SH-03) — 14/03/2025
Competitive displacement risk	3 customers actively evaluating Monday.com / Asana. If 2 of 3 churn, that is ~20M VND/month MRR loss.	CSM At-Risk List (SH-04)
Estimated total 12-month cost of inaction	~474M VND in lost/deferred revenue + compounding tech debt overhead	

3. Options Analysis

This section evaluates three strategic delivery options for Q2, comparing them across cost, benefit, risk, and alignment to business objectives BO-1 (churn reduction) and BO-2 (MRR growth).

3.1 Options Summary

Criterion	Option A: Do Nothing	Option B: Quick Wins Only	Option C: Foundation – First (Recommended)
Description	Maintain status quo. No new feature delivery in Q2.	Skip Refactor. Deliver Export Excel + Notification as quickly as possible. Defer Time Tracking.	Refactor first (2 weeks), then deliver Time Tracking + Export Excel + Bulk Action + Notification in Q2.
Q2 Features Delivered	None	Export Excel (3 wks), Notification (3–4 wks + bug risk)	Refactor (2 wks), Time Tracking (3 wks), Export Excel (3 wks), Bulk Action (1 wk), Notification (2 wks)
Total Calendar Duration	N/A	6–7 weeks (with bug risk adding unpredictable delay)	11 weeks (predictable, low bug risk)
Q2 Development Cost	0M VND (but 474M VND cost of inaction)	~78M VND (7 weeks × 4 devs × 2.8M)	~123M VND (11 weeks × 4 devs × 2.8M)
Estimated 12-month MRR Uplift	0 (negative: churn continues)	+40M to +60M VND/month (Export only)	+108M to +132M VND/month (Time Tracking + Export + Notification)
BO-1: Churn Reduction	Not addressed. Churn accelerates.	Partially addressed via Export Excel retention.	Strongly addressed: Notification reduces top complaint (18/89 tickets = 20.2%); Export secures at-risk renewals.
BO-2: MRR Growth	Not addressed. MRR stagnates/declines.	Partially addressed via Export deal closures.	Strongly addressed: Time Tracking unlocks Enterprise upsell — primary MRR growth lever for agency segment.
Technical Risk	High — debt compounding quarterly.	High — without refactor, Notification estimate is 3–4 weeks (not 2) with known bug risk in Permission Module.	Low — Refactor reduces all subsequent feature risk by 30–40%.
Recommendation	Reject	Reject	Recommended

4. Cost Analysis — Option C (Recommended)

This section details the development costs for Option C based on the engineering estimates provided by SH-03 (Tech Lead) in the meeting of 14/03/2025.

4.1 One-Time Development Costs

Featured / Activity	Duration	Developer Cost	Assumption
FT-007: Refactor Permission Module	2 weeks	22.4M VND	4 devs × 2 weeks × 2.8M VND/dev/week
FT-002: Time Tracking	3 weeks	33.6M VND	4 devs × 3 weeks × 2.8M VND/dev/week. Estimate valid only post-refactor; without refactor, this becomes 4 weeks (~44.8M VND).
FT-001: Export Excel/PDF	3 weeks	33.6M VND	4 devs × 3 weeks × 2.8M VND. MVP scope: 3 most-requested view types (pending confirmation from SH-02 — Q-02).
FT-006: Bulk Action	1 week	11.2M VND	4 devs × 1 week × 2.8M VND. Estimate valid only post-refactor.
FT-003: Notification System	2 weeks	22.4M VND	4 devs × 2 weeks × 2.8M VND. Post-refactor estimate. Without refactor: 3–4 weeks + unquantified bug risk.
Total Development Investment Q2	11 weeks	123.2M VND	Assumes 4 developers fully allocated; no external resource required in Q2.

4.2 Deferred Items (Not in Q2 Budget)

Item	Reason Deferred	Planned Quarter
FT-004: Mobile App	Minimum estimate 4 months — exceeds Q2 capacity. Churn driver #1 but requires dedicated resourcing plan.	Q3 (UX research begins late Q2 as preparatory work)
FT-005: Public API	6–8 week estimate. Requires Time Tracking to be completed first to define API data schema correctly.	Q3 (API spec design begins Q2 using 3-prospect requirements)

5. Benefit Analysis — Option C

This section quantifies the expected financial benefits of Option C, derived from prospect pipeline data (SH-02), churn data (SH-04), and customer feedback.

5.1 Quantifiable Benefits

Benefit	Month 1 – 3 (Post – delivery)	Month 4 – 6	Month 7 – 12	Annual Total	Confidence
Time Tracking: Enterprise Upsell Revenue	+20M VND/mo	+32M VND/mo	+40M VND/mo	~384M VND	Medium
Export Excel: New Deal Closures	+15M VND/mo	+25M VND/mo	+30M VND/mo	~270M VND	High
Churn Reduction: MRR Retained	+10M VND/mo	+18M VND/mo	+24M VND/mo	~192M VND	Medium
Tech Debt Savings: Faster Future Delivery	+4 wks capacity	+4 wks capacity	+4 wks capacity	~134M VND equiv.	High
Total Quantifiable Benefits	~45M VND/mo	~75M VND/mo	~94M VND/mo	~980M VND	

Confidence levels defined: High = backed by 3+ data points or confirmed prospect intention. Medium = backed by 1–2 data points or directional evidence. Low = directional only.

5.2 Non-Quantifiable Benefits

Benefit	Description
Series A readiness	MRR growth trajectory and churn reduction directly improve valuation multiples for Q4 2025 Series A raise (confirmed priority of SH-01).
Competitive positioning	Time Tracking differentiates TaskFlow from local competitor Base.vn and price-competitive Trello. Establishes "billing-to-task" positioning unique in VN market.
Internal team morale	Refactor addresses a long-standing engineering pain point; improved development velocity benefits team satisfaction and retention.
Customer satisfaction (NPS)	Notification System addresses top support complaint category (18/89 tickets = 20.2%). Expected NPS increase of 5–8 points based on category resolution rate benchmarks.

6. Financial Summary

This section consolidates the cost and benefit analysis into key financial metrics for executive decision-making.

Metric	Value	Calculation Basis
Total Investment (Option C)	Q2 123.2M VND	11 weeks × 4 developers × 2.8M VND/dev/week (blended rate: 2 senior @ 3.5M + 2 junior @ 2.1M)

Total 12-Month Benefit (Option C)	~980M VND	Time Tracking (384M) + Export (270M) + Churn Savings (192M) + Tech Debt equiv. (134M) — Section 5.1
Net Value (12-Month)	~857M VND	$980M - 123.2M = 856.8M VND$
ROI (12-Month)	~695%	$(\text{Benefits} - \text{Costs}) / \text{Costs} \times 100 = (856.8 / 123.2) \times 100$
Net Present Value (NPV)	~561M VND	PV of future cash flows (discount rate 10%/yr = 0.83%/mo) minus initial investment. PV(benefits) $\approx$ 684M at 10% annual discount rate; NPV = 684M – 123.2M = ~561M VND
Internal Rate of Return (IRR)	>200% annual	IRR exceeds 200% annually given positive cumulative cash flow achieved by Month 9 post-investment. Exact IRR calculation requires monthly cash flow model in finance system.
Estimated Payback Period	4–5 months post-delivery (Month 7–8 overall)	Investment of 123.2M recovered when cumulative benefits exceed cumulative costs (see Cash Flow Projection Section 6.1). Break-even occurs between Month 4–5 post-launch.

6.1 Monthly Cash Flow Projection

	Q2 (Months 1 – 3) Development	Month 4 – 5 Post – Launch	Month 6 – 9	Month 10 – 12	12 – Month – Trial
Development Cost	(123.2M)	0	0	0	(123.2M)
Incremental MRR	0	+45M/mo	+75M/mo	+94M/mo	~656M
Tech Debt Savings	0	+11M/mo	+11M/mo	+11M/mo	~88M equiv.
Net Cumulative	(123.2M)	(33M)	+258M	+723M	~856M

7. Risk Assessment

This section identifies risks to Option C delivery and benefit realization, with mitigation actions and owners.

Risk ID	Risk	Probability	Impact	Severity	Mitigation	Owner
R-01	Refactor scope creep — 2-week estimate expands, delaying Sprint 2 start.	Medium	High	Major	Fix scope strictly: only Permission Module. Define explicit done criteria before Sprint 1 starts. SH-03 signs off on	SH-03

					scope boundary.	
R-02	Export Excel MVP scope disagreement between Sales (wants all 12 views) and Tech (estimates 3 views = 3 weeks).	High	Medium	Major	Resolve Open Question Q-02 by 17/03/2025. Define MVP as the 3 most-requested view types. Document scope in Scope Document (Step 05).	BA + SH-02 + SH-03
R-03	Time Tracking adoption failure — team members do not log time consistently, defeating the billing use case.	Medium	High	Major	UX must prioritise 1-click time logging. CSM (SH-04) must run adoption training with customers during beta. Include adoption KPI in success metrics.	SH-04 + Product
R-04	Mobile App churn continues during Q2 while Mobile is deferred to Q3.	High	Medium	Major	Mitigate via Notification System delivery (reduces PM frustration without mobile). CSM proactively communicates Q3 Mobile roadmap to at-risk accounts. Begin Mobile UX research in Q2.	SH-04
R-05	Technical estimate uncertainty — developer productivity affected by unforeseen issues during Time Tracking build.	Low	Medium	Minor	4-developer team allows parallel workstreams. Bulk Action (1 week) acts as buffer task. BA tracks sprint velocity weekly.	SH-03 + BA

7.1 Sensitivity Analysis


Scenario	Key Assumption Change	12 Month Net Benefit	Payback Period
Best Case	All 4 Time Tracking prospects convert at 10M VND/month; Export closes 7 deals; churn drops to 2%.	~1,200M VND	3 months
Base Case (this document)	3 of 4 Time Tracking prospects convert; Export closes 5 deals; churn drops to ~2.8%.	~857M VND	4–5 months

Worst Case	Only 1 Time Tracking prospect converts; Export closes 2 deals; churn stays at 4%.	~340M VND	7–8 months
------------	---	-----------	------------

Robustness: Option C delivers positive ROI in all 3 scenarios tested. Worst case still yields ~276% ROI on 123.2M VND investment over 12 months.

8. Implementation Plan

Diagram 1: Q2 Sprint Timeline — Option C (Foundation-First)

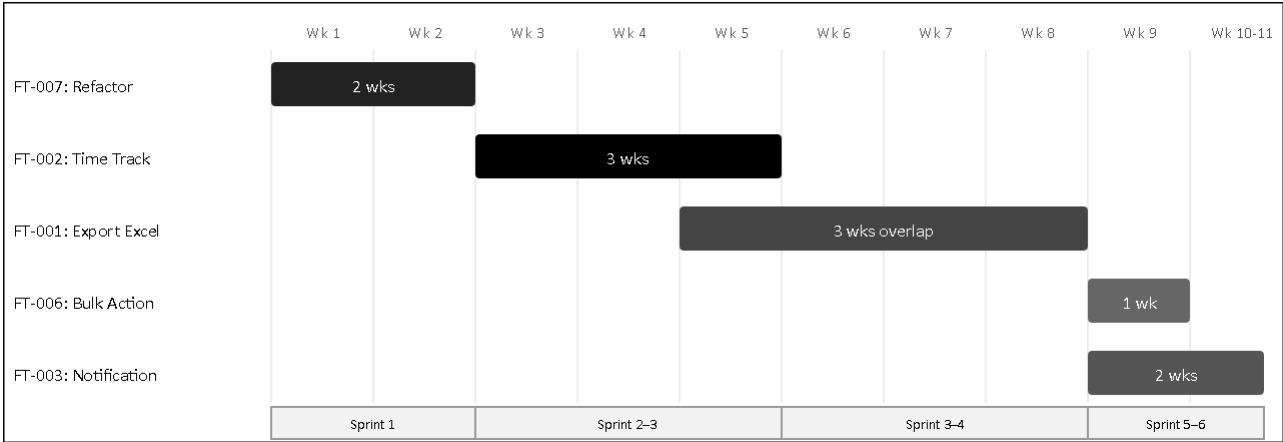

Sprint	Weeks	Focus	Milestone	Cost
Sprint 1	Wks 1–2	FT-007: Refactor Permission Module	Permission module refactored. Bug rate baseline re-measured. All subsequent features unblocked.	22.4M VND
Sprint 2–3	Wks 3–5	FT-002: Time Tracking	Beta release to 5 pilot customers. At least 1 Enterprise upgrade confirmed.	33.6M VND
Sprint 3–4	Wks 5–8	FT-001: Export Excel/PDF	MVP export (3 view types). At least 2 renewal conversations re-opened with at-risk customers.	33.6M VND
Sprint 5	Wk 9	FT-006: Bulk Action	Bulk status edit deployed. Support ticket category closes.	11.2M VND
Sprint 5–6	Wks 9–11	FT-003: Notification System	Real-time task/comment notifications deployed. Target: close top support ticket category (18 tickets resolved).	22.4M VND
Total Q2 Investment				123.2M VND

9. Recommendation

This section provides the final, justified recommendation for executive decision.

Approve Option C: Foundation-First Delivery

Option C is recommended because it is the only option that simultaneously addresses both Q2 business objectives within the available engineering capacity.

1. **Highest financial return:** 12-month net benefit of ~857M VND on 123.2M VND investment (695% ROI), with positive ROI confirmed even in worst-case scenario.
2. **Directly targets both OKRs:** Time Tracking drives MRR growth (+108M to +132M VND/month potential from Enterprise upsell); Export Excel + Notification addresses top churn and at-risk renewal triggers.
3. **Technically sound and de-risked:** The 2-week investment in Refactor reduces all subsequent Q2 delivery risk by 30–40%, making delivery timelines reliable enough to commit to customers and board.

Trade-offs accepted: Mobile App (churn driver #1) is deferred to Q3. This is mitigated by Notification System delivery and proactive CSM communication of the Q3 Mobile commitment to at-risk accounts.

Decision needed by: 18 March 2025 to begin Sprint 1 on 24 March 2025.

9.1 Assumptions & Limitations

- Developer cost rate of 2.8M VND/developer/week is blended across 2 senior (3.5M) and 2 junior (2.1M) developers.
- MRR uplift estimates for Time Tracking assume 3 of 4 identified prospects convert within 3 months of feature release. Actual conversion depends on sales execution.
- Export Excel MVP scope is assumed to cover 3 view types. Final scope must be confirmed via Open Question Q-02 (due 17/03/2025).
- Tech debt savings are estimated as engineering-time equivalents (4 weeks saved = 4 devs × 1 week × 2.8M = 11.2M VND per delayed feature cycle) and may not directly appear as MRR in financial reporting.
- **Data sources:** Guest meeting transcript (14/03/2025), Customer Feedback compilation (01/01–14/03/2025), Stakeholder Brief (15/03/2025).

10. Sign-off

Role	Name	Date Reviewed	Decision
CEO / Co-founder	Minh Khoa (SH-01)		
Head of Sales	Thu Hang (SH-02)		
Tech Lead	Bao Trung (SH-03)		

Customer Success Manager	Linh Phuong (SH-04)		
--------------------------	---------------------	--	--
