
BA Delivery Plan

for

TaskFlow Q2/2025 — Work Management Platform

Version 1.0 – Draft

Prepared by Duy Thien

Personal Project

Date: April 2026

Table of Contents

- 1. Purpose & Overview1
- 2. BA Deliverables Register1
- 3. BA Deliverables Timeline.....3
- 4. RACI Matrix3
- 5. Requirements Elicitation Plan5
- 6. Communication Plan6
- 7. BA Work Breakdown Structure (WBS).....7
- 8. BA Delivery Risk Register9
- 9. Requirements Quality Standards10
- 10. Sign-off.....11

Revision History

Name	Date	Reason For Changes	Version

1. Purpose & Overview

This section defines the purpose, coverage, and governance of this plan. The BA Delivery Plan is the operational blueprint for the BA's work across the Q2/2025 project lifecycle.

This document defines **what** the BA will deliver, **when** each deliverable is due, **who** is responsible and accountable for each artefact (RACI), **how** requirements will be elicited, and **what risks** could prevent timely delivery. It serves as the primary reference for coordinating BA activities with development sprints, stakeholder reviews, and the overall Q2 roadmap.

Important: This plan governs BA activities only. It is not the engineering sprint plan. Development estimates and sprint assignments are managed separately by SH-03 (Tech Lead) in the engineering backlog. The BA Delivery Plan feeds requirements *into* that plan.

Item	Detail
BA engagement model	Embedded BA — Duy Thien works full-time on this project throughout Q2/2025.
Q2 delivery window	24 March 2025 – 13 June 2025 (11 weeks)
Total BA deliverables	11 documents across Steps 03–09 of the BA Workflow (3 already completed)
Primary methodology	Iterative BA — requirements elicited and validated per feature in alignment with sprint cadence. Not waterfall (all requirements upfront).
Toolset	Requirements: Markdown (.md) + HTML export. Wireframes/Mockups: Stitch MCP. Diagrams: SVG inline. Tracking: project board (backlog).

2. BA Deliverables Register

This section catalogues every document the BA is responsible for producing in Q2. Each deliverable is assigned an ID, mapped to a BA Workflow step, and linked to the features it covers.


ID	Deliverable	BA Step	Covers	Status	Target Date
DOC-01	Stakeholder Matrix & Register	Step 03	All stakeholders	✓ Complete	17/03/2025
DOC-02	Business Case	Step 04	7 features, Q2 option selection	✓ Complete	17/03/2025
DOC-03	Scope Document	Step 05	5 in-scope features, boundary definition	✓ Complete	18/03/2025
DOC-04	BA Delivery Plan (this document)	Step 06	All BA activities, RACI, timeline	In Progress	19/03/2025
DOC-05	Business Requirements Document (BRD)	Step 07	FT-002, FT-001, FT-006, FT-003	Pending	26/03/2025
DOC-06	Use Cases	Step 07	FT-002, FT-001, FT-006, FT-003	Pending	28/03/2025
DOC-07	User Stories + Acceptance Criteria	Step 07	FT-002, FT-001, FT-006, FT-003	Pending	31/03/2025
DOC-08	Wireframes & UI Mockups	Step 08 — Design	FT-002, FT-001, FT-006, FT-003 (8 screens)	Pending	07/04/2025
DOC-09	Test Cases	Step 08 — Testing	FT-002, FT-001, FT-006, FT-003	Pending	25/05/2025
DOC-10	UAT Plan & UAT Sign-off	Step 08 — Deploy	All in-scope features	Pending	03/06/2025
DOC-11	Performance Report (Post-launch)	Step 09	BO-1 and BO-2 measurement	Pending	13/07/2025 (post-Q2)

Note on FT-007 (Refactor): The Refactor is a technical internal task. It does not require a dedicated BRD or User Stories. It is covered by technical documentation produced by SH-03 (Tech Lead) during Sprint 1. The

BA's role for FT-007 is to define the permission role model (Section 4.1 of the Scope Document) and validate post-refactor regression.

3. BA Deliverables Timeline

This section visualises when each BA deliverable will be produced relative to the 11-week Q2 delivery window and the corresponding engineering sprints.

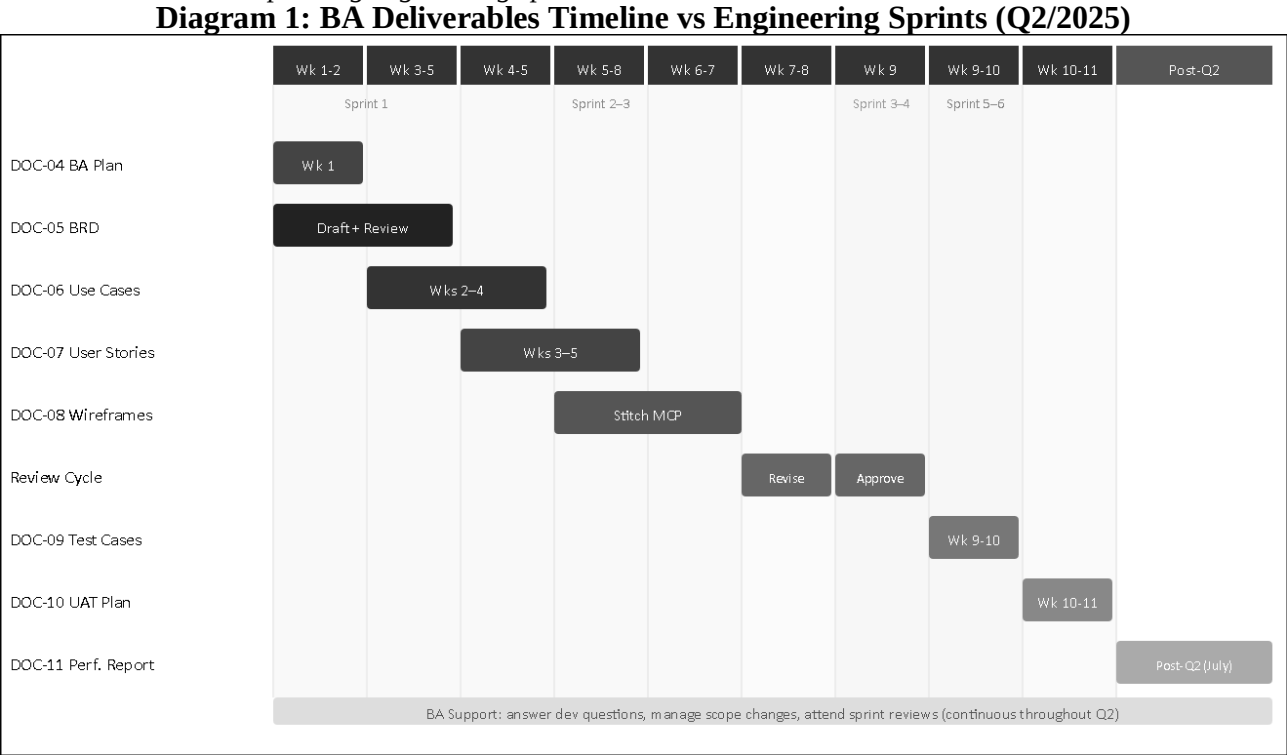

4. RACI Matrix

This matrix defines who is Responsible, Accountable, Consulted, and Informed for each BA deliverable and key project activity. It is the primary governance tool for managing sign-off and communication throughout Q2.

R — Responsible: Does the work A — Accountable: Owns the outcome, gives final approval
C — Consulted: Provides input before work is done I — Informed: Notified when done

Deliverable / Activity	SH-01 CEO	SH-02 Sales	SH-03 Tech Lead	SH-04 CSM	BA Duy Thien	Designer (TBD)	QA (TBD)
PLANNING PHASE — Steps 03-06							
DOC-01: Stakeholder Matrix	A	C	C	C	R	I	I

Deliverable / Activity	SH-01 CEO	SH-02 Sales	SH-03 Tech Lead	SH-04 CSM	BA Duy Thien	Designer (TBD)	QA (TBD)
DOC-02: Business Case	<u>A</u>	C	C	C	R	I	I
DOC-03: Scope Document	<u>A</u>	C	<u>A</u>	C	R	I	I
DOC-04: BA Delivery Plan (this)	<u>A</u>	I	C	I	R	I	I
REQUIREMENTS DEFINITION PHASE — Step 07							
DOC-05: Business Requirements Document (BRD)	<u>A</u>	C	C	C	R	I	I
DOC-06: Use Cases	I	I	<u>A</u>	C	R	C	C
DOC-07: User Stories + Acceptance Criteria	I	C	<u>A</u>	C	R	C	C
Requirements Elicitation Workshops	C	C	C	C	R	I	I
Scope Change Request evaluation	<u>A</u>	I	C	I	R	I	I
DESIGN PHASE — Step 08 (Design)							
DOC-08: Wireframes & Mockups (via Stitch MCP)	<u>A</u>	C	C	C	R	R	I
Wireframe review and validation with stakeholders	<u>A</u>	C	C	C	R	R	I
BUILD & TEST PHASE — Step 08 (Code / Test)							
Requirements clarification during development	I	I	C	I	R	I	I
DOC-09: Test Cases	I	I	<u>A</u>	C	R	I	R
DOC-10: UAT Plan & Execution	<u>A</u>	I	C	R	R	I	C
UAT Sign-off with pilot customers	<u>A</u>	I	I	R	C	I	I
POST-LAUNCH — Step 09							
DOC-11: Performance Report (BO-1 & BO-2 measurement)	<u>A</u>	C	I	C	R	I	I
Enhancement / new project trigger (Decision Gate 2)	<u>A</u>	C	C	C	R	I	I

Double Accountable (DOC-03): SH-01 (CEO) is accountable for business scope decisions (what features are in/out). SH-03 (Tech Lead) is accountable for technical feasibility of scope boundaries. Both must sign off on the Scope Document. In case of conflict, SH-01 has final authority.

5. Requirements Elicitation Plan

This section defines how the BA will gather, validate, and confirm requirements for each in-scope feature. Different elicitation techniques are used depending on the feature type and information needed.

Feature	Elicitation Technique	Participants	Output	Scheduled
FT-002: Time Tracking	Document Analysis: Review Email 05 (agency billing pain point) and customer feedback already collected. Structured Interview: 1-on-1 session with SH-02 (Sales) to map the exact agency billing workflow — from task creation to client invoice. Prototype Validation: Show wireframe (DOC-08 WF-01) to 2 pilot agency directors before dev begins. Validate timer UX and billing summary layout.	SH-02, SH-04, 2 pilot customers	BRD Section for FT-002; Use Cases UC-001 to UC-004; User Stories US-001 to US-008	Wk 1–2 (Sprints 1)
FT-001: Export Excel/PDF	Document Analysis: Review Email 02 (export for weekly client report) and Sales pipeline data (5 blocked prospects). Workshop: Joint session with SH-02 (Sales) + SH-04 (CSM) — define the 3 MVP view types and exact column requirements for each. Required to resolve Open Question Q-02. Prototype Validation: Show PDF export mockup (DOC-08 MK-01) to 1 at-risk customer for feedback.	SH-02, SH-04, SH-03, 1 at-risk customer	BRD Section for FT-001; Use Cases UC-005 to UC-007; User Stories US-009 to US-014	Wk 2 (after Q-02 resolved)
FT-003: Notification System	Document Analysis: 18 support ticket descriptions from CSM report — extract exact trigger patterns and user frustration points. Structured Interview: 30-min session with SH-04 (CSM) — review top 5 ticket examples verbatim; confirm whether email or in-app is the primary channel	SH-04, SH-03	BRD Section for FT-003; Use Cases UC-008 to UC-011; User Stories US-015 to US-020	Wk 2–3

Feature	Elicitation Technique	Participants	Output	Scheduled
	for each trigger type.			
FT-006: Bulk Action	Document Analysis: Email 04 (sprint-end bulk status change) + 11 additional similar requests from CSM note. Observation (informal): Ask 1 PM pilot customer to walk through their end-of-sprint process on current TaskFlow. Record what manual steps are taken. Identify all candidate bulk operations.	SH-04, 1 PM pilot customer	BRD Section for FT-006; Use Cases UC-012 to UC-014; User Stories US-021 to US-025	Wk 2

6. Communication Plan

This section defines how the BA will maintain alignment with all stakeholders throughout Q2. Regular communication prevents requirement drift, missed sign-offs, and late-stage scope surprises.

Communication	Audience	Frequency	Format	Owner	Purpose
BA Status Update	SH-01 (CEO)	Weekly (Monday)	Written summary (email/doc comment) — max 1 page	BA	Report deliverable status, flag blockers, escalate open questions past their deadline.
Requirements Review Session	SH-02, SH-03, SH-04	Per deliverable (before sign-off)	60-minute walkthrough meeting. BA presents; stakeholders review and comment.	BA	Validate requirements in DOC-05, DOC-06, DOC-07 before passing to development.
Sprint Planning Participation	SH-03 + Dev team	Every 2 weeks (Sprint start)	Attend sprint planning. BA confirms requirements are complete and unambiguous for sprint backlog items.	BA	Ensure developers have all requirements before committing to sprint. Prevent mid-sprint requirement discovery.
Sprint Review Participation	SH-01, SH-02, SH-04	Every 2 weeks (Sprint end)	Demo review. BA verifies delivered features match acceptance criteria in User Stories.	BA	Early detection of requirement misalignment before final release.

Communication	Audience	Frequency	Format	Owner	Purpose
Elicitation Workshop	Per feature (see Section 5)	Once per feature (Wk 1–3)	Structured 60–90 min session. BA facilitates; records outcomes in meeting notes.	BA	Gather detailed requirements before BRD drafting. Resolve ambiguities early.
Open Question Tracker	All stakeholders	Updated within 24h of any change	Shared document. BA tracks Q-01 to Q-05 (and any new questions) with owner, deadline, and resolution status.	BA	Ensure no open question remains unresolved past its deadline and blocks delivery.

7. BA Work Breakdown Structure (WBS)

This section breaks down the BA's tasks into an estimated effort schedule. Effort is measured in BA working days (1 day = 8 hours).

Task	Feature / Area	Effort (days)	Target Week	Dependency
Phase 1: Planning (Completed)				
DOC-01 Stakeholder Matrix	All	1.5	Wk 0 (pre-Q2)	None
DOC-02 Business Case	All 7 features	2	Wk 0 (pre-Q2)	DOC-01
DOC-03 Scope Document	5 in-scope features	2	Wk 0 (pre-Q2)	DOC-02
DOC-04 BA Delivery Plan	All	1	Wk 1	DOC-03
Phase 2: Requirements Definition (Wk 1–5)				
Elicitation workshops (4 sessions)	FT-001, FT-002, FT-003, FT-006	4	Wk 1–3	DOC-04

Task	Feature / Area	Effort (days)	Target Week	Dependency
Pilot customer interviews (3 sessions)	FT-001, FT-002	2	Wk 2–3	Elicitation workshops
DOC-05 BRD — Draft	FT-001, FT-002, FT-003, FT-006	4	Wk 2–4	Elicitation complete
DOC-05 BRD — Review cycle + revisions	All	2	Wk 4–5	BRD Draft
DOC-06 Use Cases	FT-001, FT-002, FT-003, FT-006	3	Wk 3–4	BRD Draft
DOC-07 User Stories + Acceptance Criteria	FT-001, FT-002, FT-003, FT-006	3	Wk 4–5	Use Cases
Phase 3: Design Validation (Wk 4–7)				
DOC-08 Wireframes — brief preparation	8 screens (see Scope Doc)	1	Wk 4	User Stories
DOC-08 Wireframe generation (Stitch MCP)	8 screens	2	Wk 5–6	Brief prepared
DOC-08 Wireframe review with stakeholders	All	2	Wk 6–7	Wireframes generated
Phase 4: Build Support (Wk 1–11, continuous)				
Sprint planning participation (6 sprints)	All	3	Wk 1–11	Ongoing
Sprint review participation (6 sprints)	All	3	Wk 2–11	Ongoing
Requirements clarification	All	5	Wk 1–11	Ongoing

Task	Feature / Area	Effort (days)	Target Week	Dependency
(ad-hoc dev Q&A)				
Scope change evaluation (if any)	All	2	On request	Ongoing
Phase 5: Testing & Launch (Wk 9–11)				
DOC-09 Test Cases	FT-001, FT-002, FT-003, FT-006	3	Wk 9–10	Dev near-complete
DOC-10 UAT Plan + facilitation	All in-scope	3	Wk 10–11	Test Cases
Phase 6: Post-Launch (July 2025)				
DOC-11 Performance Report	BO-1, BO-2 measurement	3	Post-Q2	4 weeks post-launch data
Total BA Effort Estimate		47 days (~9.4 weeks)		

8. BA Delivery Risk Register

This section identifies risks specific to BA delivery activities (not engineering risks, which are managed in the engineering plan). Each risk is assigned a probability, impact rating, and a concrete mitigation action.

ID	Risk	Prob.	Impact	Severity	Mitigation	Owner
BR-01	Open Question Q-02 (Export scope: 3 vs 12 views) not resolved by 17/03/2025. FT-001 BRD cannot be drafted.	High	High	Critical	BA escalates to SH-01 (CEO) the morning of 17/03 if not resolved. CEO makes final call. BA documents decision and proceeds.	BA → SH-01
BR-02	Stakeholder unavailability for requirements	Medium	High	Major	All review sessions are scheduled at least 5 working days in advance. If SH	BA

ID	Risk	Prob.	Impact	Severity	Mitigation	Owner
	review — sign-off on DOC-05 BRD delayed, blocking dev start.				unavailable, delegate to next accountable person (per RACI). Async review (written comments) accepted as alternative.	
BR-03	Scope creep — stakeholder (likely SH-02 Sales) requests new features mid-Q2 citing urgent customer pressure.	High	High	Major	Apply formal scope change process (Scope Document Section 9). BA quantifies trade-off and escalates to SH-01. No development of unscoped features is permitted regardless of stakeholder seniority.	BA → SH-01
BR-04	Pilot customer unavailability for wireframe validation — mockups shipped to dev without user validation.	Medium	Medium	Moderate	Identify 3 pilot customers during Wk 1 (with SH-04 CSM). Schedule wireframe review for Wk 6. If customer unavailable, SH-04 proxies as domain expert reviewer. Flag assumption in design sign-off.	SH-04 + BA
BR-05	Ambiguous acceptance criteria — developers interpret requirements differently; features built do not match user expectations.	Medium	High	Major	Every User Story must have Given/When/Then acceptance criteria (documented in DOC-07). BA attends Sprint Review explicitly to verify acceptance criteria are met before sprint close-out. Any mismatch is logged as a backlog defect, not a new requirement.	BA
BR-06	Wireframe iteration cycles too long — Stitch MCP revisions require multiple rounds; design delays block dev start.	Low	Medium	Moderate	Maximum 2 revision rounds per wireframe. BA prepares a detailed wireframe brief (feature scope + role matrix + key flows) before invoking Stitch MCP. Third revision round requires SH-01 written approval to change scope.	BA

9. Requirements Quality Standards

All BA deliverables must meet the following quality criteria before being submitted for stakeholder review. The BA self-reviews against this checklist before circulating any document.

#	Quality Criterion	Verification Method
---	-------------------	---------------------

#	Quality Criterion	Verification Method
Q-STD-01	Every Functional Requirement is written as "The system shall..." (mandatory) or "The system should..." (preferred). No vague language.	BA line-by-line self-review using Requirements Checklist (requirements-main/src/requirements-checklist.md)
Q-STD-02	Every requirement is testable. A corresponding test case (DOC-09) must be writable from it.	QA team confirms testability before BRD final sign-off.
Q-STD-03	Every requirement has a unique ID (FR-001, NFR-001, etc.) and traces to a Business Objective (BO-1 or BO-2).	Traceability matrix included in BRD appendix.
Q-STD-04	Every User Story follows the format: "As a [role], I want [capability], so that [benefit]." Acceptance criteria follow Given/When/Then format.	BA template enforced in DOC-07.
Q-STD-05	All documents conform to Company Rules: English language, black/white format, no emoji, proper header/footer, section numbering, and correct ID prefixes.	Final review by BA before distribution. Rules defined in rules/company-rules.md.
Q-STD-06	No requirement describes implementation details (HOW the system works). Requirements describe observable behaviour only (WHAT the system does).	Tech Lead (SH-03) flags any HOW violations during review cycle.
Q-STD-07	All roles (Owner, Admin, PM, Member, Client) are covered in every feature's requirements. No role omitted.	Role Permission Matrix in Scope Document Section 6 used as checklist for BRD completion.

10. Sign-off

Once this BA Delivery Plan is approved, the BA proceeds to define requirements (Step 07 — BRD, Use Cases, User Stories). This plan is the governance baseline for all BA activity in Q2.

Role	Name	Date Reviewed	Decision (Approve / Reject / Revise)
CEO / Co-founder	Minh Khoa (SH-01)		
Tech Lead	Bao Trung (SH-03)		
Customer Success Manager	Linh Phuong (SH-04)		
