
Scope Document Q2/2025

for

TaskFlow Q2/2025 — Work Management Platform

Version 1.0 – Draft

Prepared by Duy Thien

Personal Project

Date: Apr 2026

Table of Contents

- 1. Executive Summary1
- 2. Scope Objectives & Business Traceability.....1
- 3. System Context Diagram.....2
- 4. In-Scope Definition Per Feature2
 - 4.1 FT-007: Refactor Permission Module 2
 - 4.2 FT-002: Time Tracking 3
- 5. Out-of-Scope Definition (Q2)10
- 6. User Role Permission Matrix (Q2)11
- 7. Feature Dependency Map12
- 8. Assumptions & Constraints12
 - 8.1 Assumptions 13
 - 8.2 Constraints..... 13
- 9. Scope Change Control Process14
- 10. Open Questions (Scope-Blocking)14

Revision History

Name	Date	Reason For Changes	Version

1. Executive Summary

This section summarises the scope baseline derived from approved Business Case Option C and defines what is in and out of scope for Q2/2025.

Item	Detail
Scope basis	Business Case Option C approved. All scope decisions derive from that approval.
Q2 delivery window	24 March 2025 – 13 June 2025 (11 weeks / 6 sprints)
In-scope features (5)	FT-007 Refactor, FT-002 Time Tracking, FT-001 Export Excel/PDF, FT-006 Bulk Action, FT-003 Notification System
Out-of-scope (Q2)	FT-004 Mobile App, FT-005 Public API — deferred to Q3
Team	4 developers (2 senior, 2 junior). No external resource in Q2.
Hard dependency	FT-007 (Refactor) must complete before FT-002, FT-003, FT-006 can begin.
Scope change rule	All additions require written approval: SH-01 (CEO) + SH-03 estimate. No verbal changes accepted.

2. Scope Objectives & Business Traceability


Every in-scope item must trace to BO-1 (Churn <3%) or BO-2 (MRR +25%). Items with no traceability are candidates for deferral.

Feature	Traces to	Business Justification
FT-007: Refactor	BO-1 + BO-2 (Enabler)	Without refactor, every Q2 feature costs 30–40% extra dev time. Technical prerequisite for reliable delivery.
FT-002: Time Tracking	BO-2 (Primary)	4 prospects ready to upgrade to Enterprise. Estimated +32M–40M VND/month MRR uplift. Core billing feature for agency segment.
FT-001: Export Excel/PDF	BO-1 + BO-2	1 confirmed churn + 3 at-risk accounts + 5 prospects (180M VND/year pipeline). Weekly client reporting is mandatory for agencies.
FT-006: Bulk Action	BO-1 (Supporting)	22 customer requests (11 tickets + 11 similar). Quick win (1 week). Reduces PM daily friction and support ticket volume.
FT-003: Notification System	BO-1 (Primary)	18/89 Q1 support tickets (20.2%). Top complaint category. Eliminates PM dependency on Zalo for task status updates.

3. System Context Diagram

This section defines the TaskFlow system boundary and all external actors/systems it interacts with in Q2. Dashed connections indicate Q3 out-of-scope relationships.

Diagram 1: System Context — TaskFlow Q2 Boundary (Level 0)

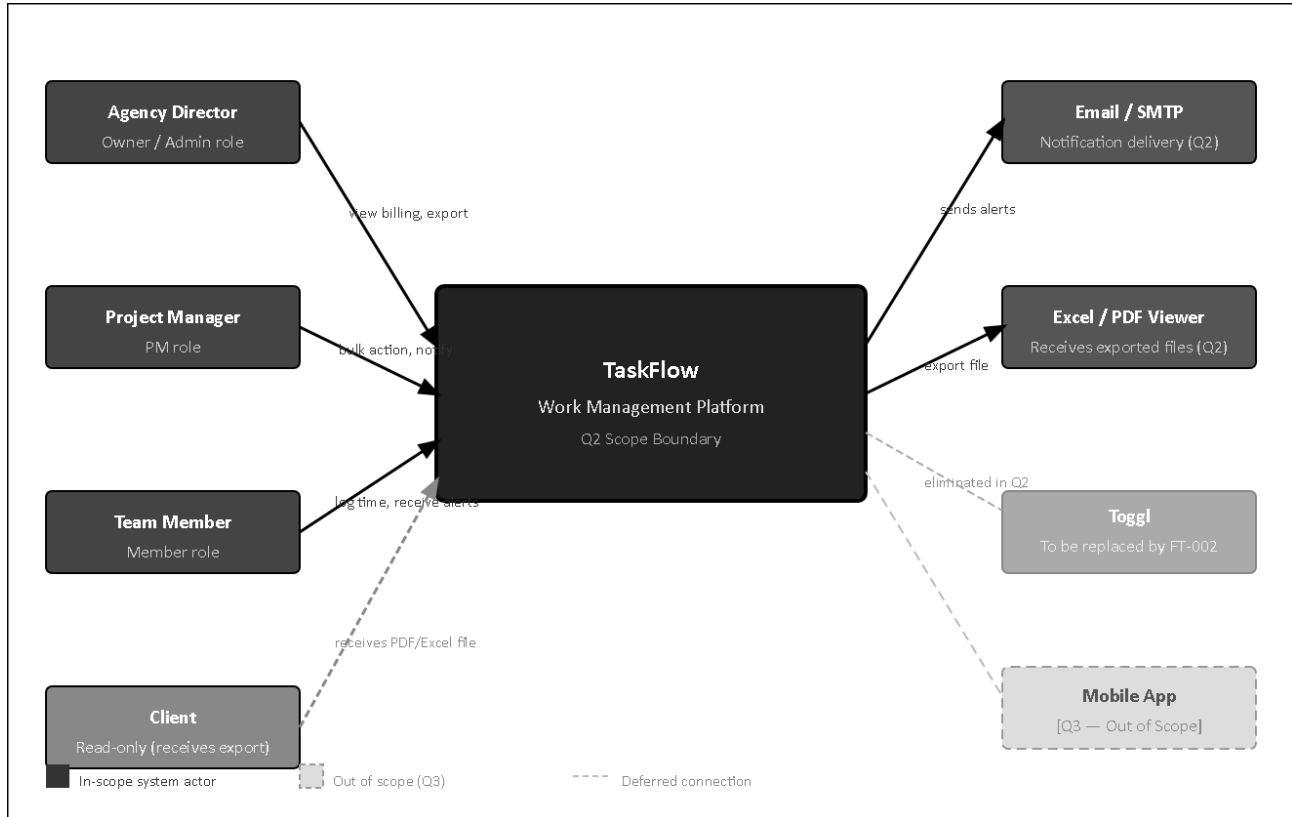


4. In-Scope Definition Per Feature

This section defines the precise MVP boundary of each in-scope feature — what is included and what is explicitly excluded from Q2 delivery.

4.1 FT-007: Refactor Permission Module

Nature: Internal technical task. No user-visible UI changes. Sprint 1 prerequisite.

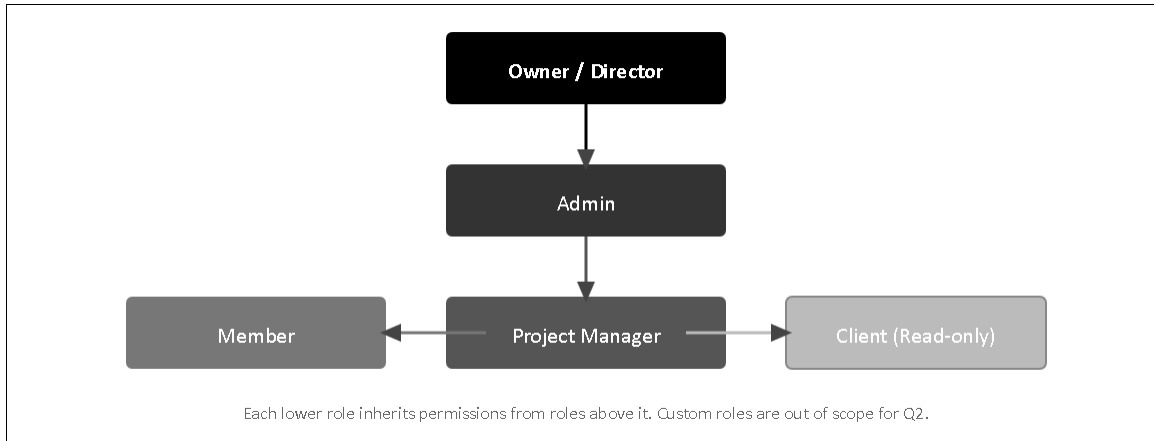Diagram 2: Permission Role Hierarchy — 5 Fixed Roles (Q2 Scope)

In Scope (Q2)	Out of Scope (Q2)
- Re-architecture of Permission Module to remove structural bugs. 5 fixed roles: Owner, Admin, Project Manager, Member, Client (read-only). - Regression testing on all existing features post-refactor. - Developer documentation of new permission model.	- New permission roles beyond the 5 defined. - Custom role creation by users — deferred. - Permission audit log / change history — deferred. - UI-level permission management screen redesign — deferred.

4.2 FT-002: Time Tracking

Primary users: Team Member (logs time), Project Manager (reviews team logs), Agency Director (views billing summary).

In Scope (Q2 MVP)	Out of Scope (Q2)
- Manual time entry per task: start time, end time, or direct duration. - Start/stop timer on task detail view — one active timer per user at a time. - Time log history per task: all entries by assignees. - Project-level time summary: total hours logged per member. - Client billing summary: billable hours × hourly rate per project (one rate per project in MVP). - Basic Excel export of time logs (team member, task, hours, date). - Permission: Owner/Admin view billing summaries; Members view own logs only.	- Automatic time tracking (activity monitoring) — deferred. - Toggl API integration — deferred to Q3 with Public API. - Invoice / PDF billing document generation — deferred to Q3. - Manager approval workflow for time entries — deferred. - Mobile time tracking — requires Mobile App (Q3). - Time analytics dashboard with charts — deferred. - Multiple hourly rates per task — deferred; one rate per project in MVP.

Wireframe: FT-002-WF-01 — Time Tracking — Task Detail View

TASK_DETAILBLUEPRINT V.01

ACTION 1ACTION 2X⋮

PROJECT_ALPHA
V.01

DASHBOARD

TASKS

CALENDAR

SETTINGS

NEW_TASK

TASK_IDENTIFIER: ALPHA-001

TASK TITLE PLACEHOLDER

TASK DESCRIPTION AREA

SKELETAL_STRUCTURE_VIEW

SUBTASKS_REGISTRY

COMMENT/ACTIVITY FEED

TIME TRACKING WIDGET

[00:00:00]

START TIMER TOGGLE

RECENT LOGS

SYSTEM_METADATA

ASSIGNEEUNASSIGNED

DATE_CREATED2023_10_24

STATUSDRAFT

Wireframe: FT-002-WF-02 — Time Tracking — Client Billing Summary View

BILLING_SYS
V1.0_BLUEPRINT

DASHBOARD

PROJECTS

INVOICES

CLIENTS

SETTINGS

HELP

LOGOUT

CLIENT BILLING SUMMARY PLACEHOLDER

SELECT PROJECT [V]

DATE RANGE

EXPORT_CSV

GENERATE_REPORT

USER	TASK	DATE	LOGGED HOURS	RATE	SUBTOTAL
A. ARCHITECT	Structural Analysis	2023-10-24	8.5 hr	\$120.00	\$1,020.00
B. ENGINEER	Blueprint Revision	2023-10-25	4.0 hr	\$95.00	\$380.00
C. DRAFTSMAN	CAD Modeling	2023-10-25	12.0 hr	\$65.00	\$780.00
A. ARCHITECT	Site Inspection	2023-10-26	6.0 hr	\$120.00	\$720.00
D. PROJECT MGR	Budget Audit	2023-10-27	3.5 hr	\$150.00	\$525.00

INVOICE SUMMARY

TOTAL HOURS

[34.0 hr]

TOTAL AMOUNT

[\$3,425.00]

EXPORT PDF/EXCEL (ACTION)

BLUEPRINT SPECS

PROJECT: #0092-ALPHA

STATUS: DRAFT_UNSTAGED

ENCODING: UTF-8_STANDARD

AUTH: ADMIN_SECURED

SYSTEM_REF: BILL-2023-PX99 // NO SHADOWS APPLIED


RENDERED @ 100% SCALE // 90° ANGULAR ALIGNMENT

4.3 FT-001: Export Excel/PDF

Primary users: Project Manager (weekly client reports), Agency Director (project status for board review). MVP = 3 view types only (pending Q-02 confirmation).

In Scope (Q2 MVP — 3 View Types)	Out of Scope (Q2)
• View 1 — Task List Export: Task name, Assignee, Status, Due Date, Priority. Formats: .xlsx + .pdf. • View 2 — Project Progress Summary: % completion, on-track/delayed flag, open blockers. Format: .pdf (client-shareable). • View 3 — Team Workload Export: Tasks grouped by assignee with hours logged (if FT-002 active). Format: .xlsx. • User selects date range before export. • Export triggered manually from project menu. • Permission: PM and above can export; Members and Client cannot.	• Scheduled / auto-email report delivery — deferred. • Custom report builder — deferred. • Export of views 4–12 (Gantt, Budget, etc.) — deferred to Q3. • White-label PDF with client's own branding — deferred. • In-browser print preview — deferred (download-only in MVP).

Wireframe: FT-001-WF-01 — Export Modal — Project Menu

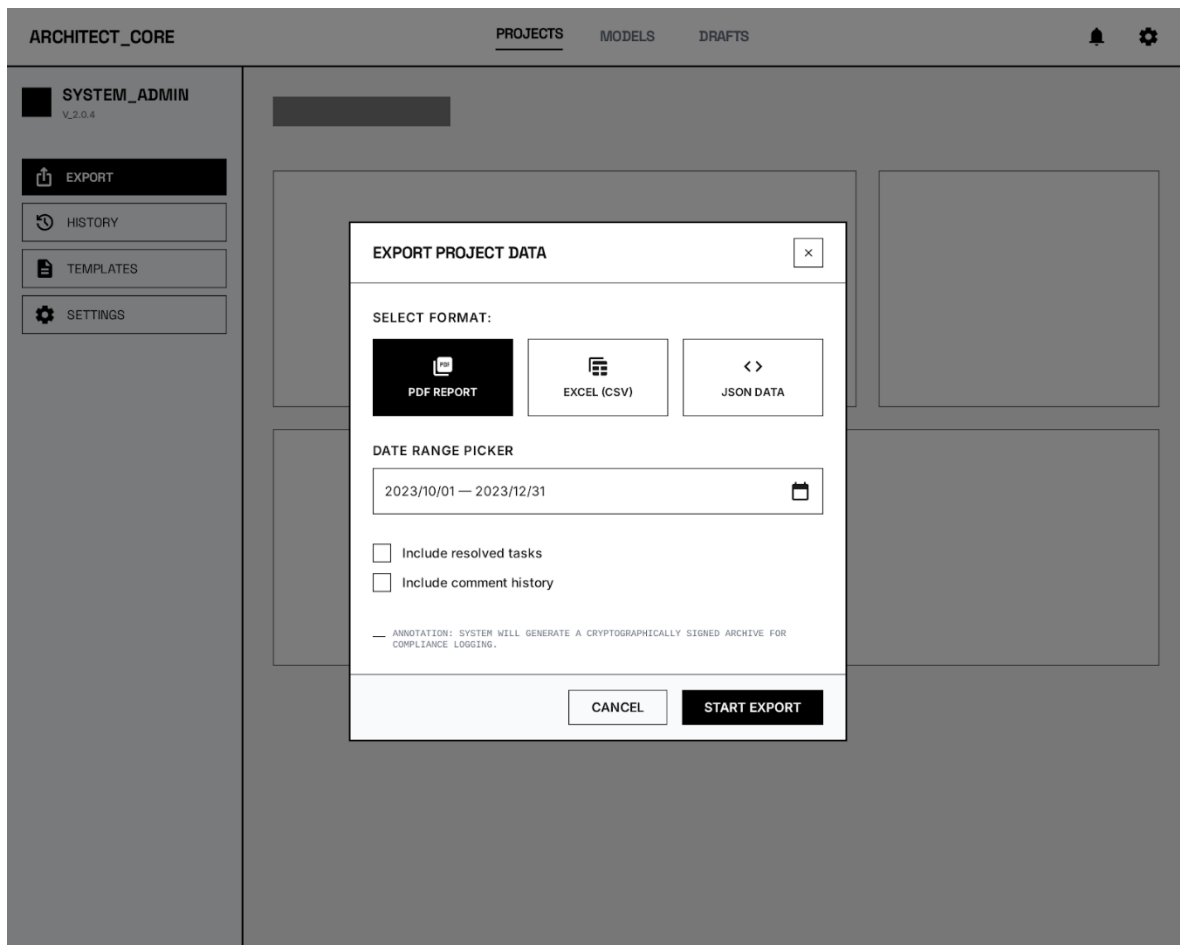

Mockup: FT-001-MK-01 — PDF Export — Project Progress Summary

Project Status Report

OverviewFinancialsTimelineResources

CalendarShareUser

TF

TaskFlow

Confidential

Ref: TF-Q4-0822

Project Status Report

GENERATED DATE: OCTOBER 24, 2023

Executive Summary

A high-level overview of the current developmental sprint cycle, tracking throughput and delivery efficiency for the Enterprise Tier.

83% Success

Cycle Velocity

Ahead of Schedule

2.4d

Avg Completion Time

120

TOTAL TASKS

100

COMPLETED

PROGRESS TRAJECTORY

+12% vs last month

Task Breakdown

OCTOBER 2023 LOG

TASK NAME	STATUS	TIME LOGGED
Initial API Architecture Design	Completed	12h 30m
Security Protocol Audit	Completed	08h 15m
Bento Grid Layout Implementation	In Progress	16h 45m
Visual Token Configuration	Completed	04h 00m
Asymmetric Grid Logic	Completed	09h 50m
Stakeholder Review Cycle	Pending	02h 20m

TaskFlow Executive Systems v4.2

Internal Use Only

Encrypted Report

Page 01 of 12

<

Document Preview: Page 1

>

Download

4.4 FT-006: Bulk Action

Primary users: Project Manager (sprint-end update), Team Member (self-status update for multiple tasks).

In Scope (Q2 MVP)	Out of Scope (Q2)
- Multi-select via checkbox in Task List view. - Bulk actions: Change Status, Reassign Assignee, Change Due Date, Delete (with confirm prompt). "Select All" checkbox in column header. - Confirmation prompt before execution: "You are about to change [N] tasks. Confirm?" - Permission: Members bulk-edit own tasks only; PM+ bulk-edit all tasks in their projects.	- Bulk action across multiple projects — deferred. - Bulk tagging or labelling — deferred. - Undo bulk action — deferred (confirmation only in MVP). - Bulk export of selected tasks — deferred.

Wireframe: FT-006-WF-01 — Bulk Action — Task List Multi-Select

[PROJECT NAME] > TASK LIST

Q SEARCH_TASKS...⚙️❓

PROJECT_CORE
V1.0.4-STABLE

NEW_ENTRY

DASHBOARD

ALL TASKS

PROJECT ARCHIVE

TEAM SPECS

SYSTEM LOGS

SETTINGS

ACTIVE_QUEUE

Review and manage structural project milestones.

SEL	TASK_IDENTIFIER	ASSIGNED_UNIT	TEMPORAL_DEADLINE
☒	[TASK_TITLE_01]	[ASSIGNEE_BOX]	[DUE_DATE_BOX]
☒	[TASK_TITLE_02]	[ASSIGNEE_BOX]	[DUE_DATE_BOX]
☒	[TASK_TITLE_03]	[ASSIGNEE_BOX]	[DUE_DATE_BOX]
☐	[TASK_TITLE_04]	[ASSIGNEE_BOX]	[DUE_DATE_BOX]
☐	[TASK_TITLE_05]	[ASSIGNEE_BOX]	[DUE_DATE_BOX]

METADATA_STREAM

3 TASKS
SELECTED

[ASSIGN]

[CHANGE
STATUS]

[DELETE]

×


DATA_X

4.5 FT-003: Notification System


Primary users: Project Manager and Team Member (real-time alerts on task events).

In Scope (Q2 MVP)	Out of Scope (Q2)
• Trigger events: (a) Task assigned, (b) Task overdue, (c) Comment added on watched task, (d) Task status changed by another member. • In-app notification centre: bell icon, unread badge, notification feed, mark-as-read. • Email notification: one email per event. User can opt out per trigger type. • Notification preference panel in user settings (toggle per trigger × channel). • Permission: Users notified only for projects they are members of. Client role receives no notifications in Q2 MVP.	• Zalo / Slack integration — deferred to Q3 with Public API. • Browser push notifications — deferred. • Digest / summary email (daily/weekly rollup) — deferred. • @mention notifications in comments — deferred. • Mobile push notifications — requires Mobile App (Q3). • Client (read-only) role email notifications — deferred.

Wireframe: FT-003-WF-01 — Notification Centre — In-App Bell Dropdown

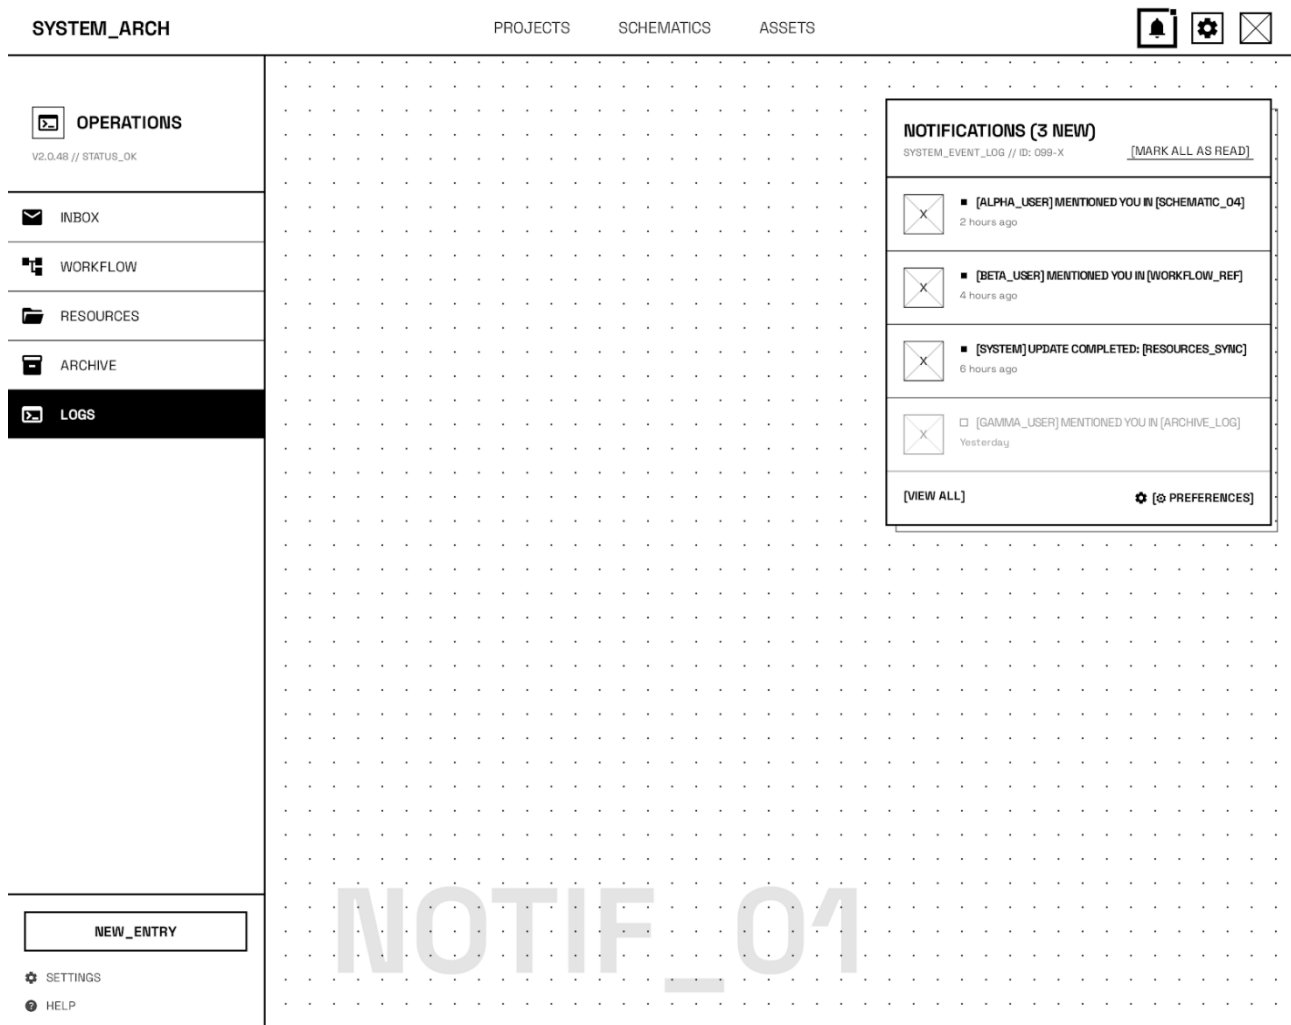

Wireframe: FT-003-WF-02 — Notification Preference Panel — User Settings

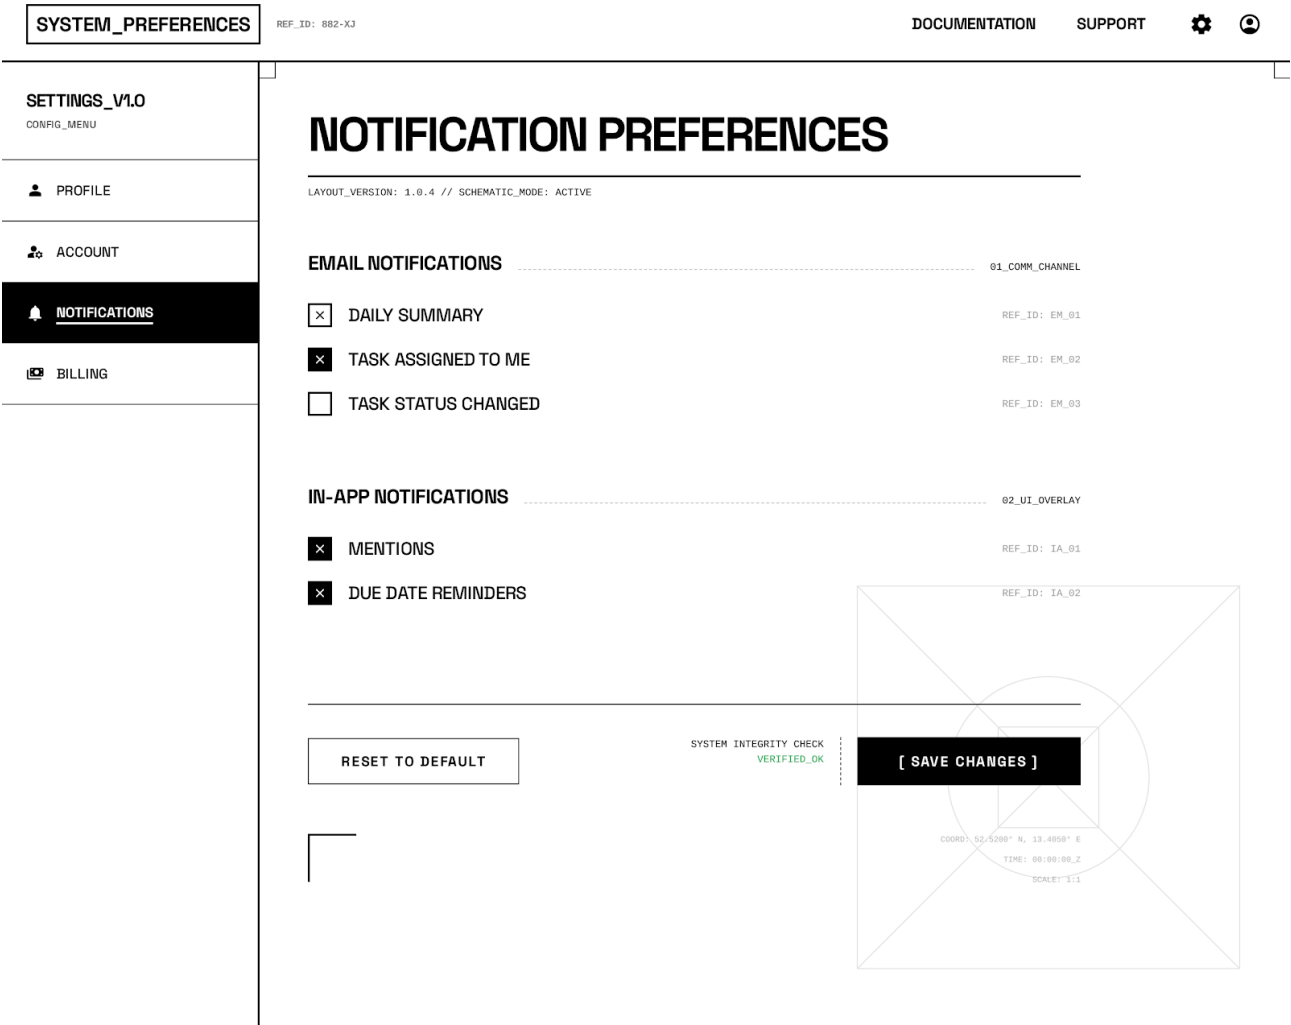

5. Out-of-Scope Definition (Q2)

All items below are explicitly excluded from Q2. Any inclusion requires a formal scope change request per Section 9.

Feature/ Capability	Reason Deferred	Risk if Not Addressed	Planned Review
T-004: Mobile App	Minimum 4-month estimate — exceeds Q2 window.	High — churn driver #1 (4 of 6 Q1 churns). Mitigation: CSM communicates Q3 commitment to at-risk accounts. Begin UX research late Q2.	Q3 Sprint 1 (June 2025)
FT-005: Public	6–8 week estimate. API	Medium — 3 enterprise prospects	Q3 Sprint 1

API	schema must follow Time Tracking finalisation to avoid rework.	(240M VND/year) require API. Mitigation: collect API requirements from prospects during Q2.	(June 2025)
Invoice / billing document generation	Depends on FT-002. Legal/accounting format requirements need separate analysis.	Low — agencies use separate accounting software for invoices.	Q3 (with Public API)
Custom permission roles	Refactor covers 5 fixed roles only. Custom roles require dedicated design sprint.	Low — no Q1 ticket evidence of demand.	Q3 Planning
Scheduled / automated report delivery	Requires background job scheduler not yet in infrastructure.	Low — manual export sufficient for MVP use case.	Q3 Planning
Any unlisted feature	Out of scope by default. Formal change request required.	N/A — change control process applies.	On request

6. User Role Permission Matrix (Q2)


This is the authoritative definition of what each role can do across all in-scope Q2 features. Used by Sprint 1 design and development.

Role	FT-002: Time Tracking	FT-001: Export	FT-006: Bulk Action	FT-003: Notifications
Owner / Director	View all logs; view all billing summaries; edit project hourly rates.	Export all 3 view types, any project.	Bulk-edit all tasks, all projects.	All trigger types. Configurable per preference.
Admin	View all logs; view billing summaries; cannot edit rates.	Export all 3 view types for assigned projects.	Bulk-edit all tasks in assigned projects.	All trigger types for assigned projects.
Project Manager	View team logs for own projects; no billing summary access.	Export all 3 view types for own projects.	Bulk-edit all tasks in own projects.	Overdue, assignment, comment, status-change for own projects.
Member	Log time on own assigned tasks; view own logs only.	Cannot export.	Bulk-edit own assigned tasks only.	Assignment + comment alerts for own tasks only.
Client (read-only)	No access.	No access (PM exports and shares file externally).	No access.	No notifications in Q2 MVP.

7. Feature Dependency Map

This section shows which features depend on other features and determines the sprint sequencing. Hard dependencies cannot be bypassed without formal technical review by SH-03.

Diagram 3: Feature Dependency Flow — Q2 In-Scope + Q3 Downstream

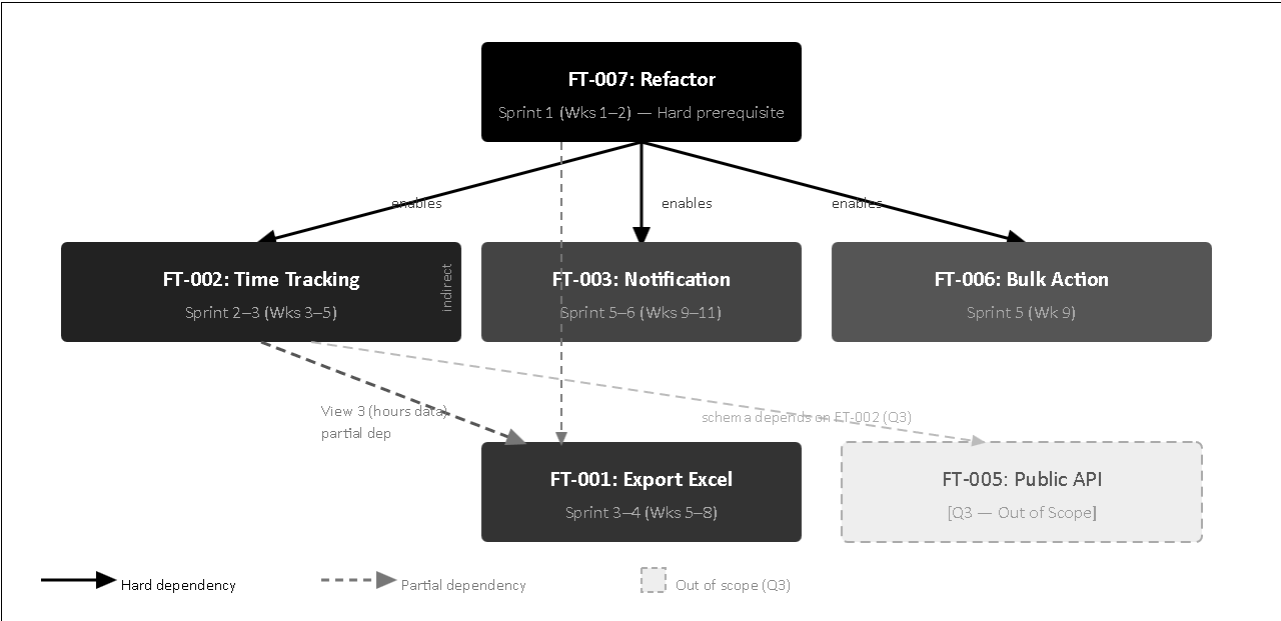

Feature	Depends On	Enables (Downstream)	Can Start Without?
FT-007: Refactor	None	FT-002, FT-003, FT-006	Yes — Sprint 1 start immediately
FT-002: Time Tracking	FT-007 (hard)	FT-001 View 3 (hours data); FT-005 API schema (Q3)	No
FT-001: Export Excel/PDF	FT-007 (indirect). Views 1 & 2 can start before FT-002; View 3 (workload + hours) requires FT-002.	None in Q2	Partial (Views 1 & 2 only)
FT-006: Bulk Action	FT-007 (hard)	None in Q2	No
FT-003: Notification System	FT-007 (hard)	None in Q2	No

8. Assumptions & Constraints

These are conditions assumed to be true and constraints that limit Q2 scope. Violating any assumption triggers formal scope re-evaluation.

8.1 Assumptions

ID	Assumption	If Violated
A-01	Export Excel MVP covers 3 view types only. Open Question Q-02 must be resolved by 17/03/2025.	12 view types required → estimate increases from 3 to 7–8 weeks; Business Case ROI changes materially; scope must be renegotiated.
A-02	Refactor scoped to 5 fixed roles and 2 weeks maximum. No new permission logic in Sprint 1.	Scope expansion cascades delay into Sprint 2 and compresses Time Tracking timeline.
A-03	4 developers fully allocated to Q2. No parallel projects will reduce team capacity below 80% per sprint.	Reduced capacity requires sprint-by-sprint re-prioritisation with SH-01 + SH-03 written approval.
A-04	Email notification infrastructure (SMTP or transactional email service) is already in place or can be provisioned within Sprint 1 at no additional cost.	If infrastructure must be procured, SH-01 must approve additional budget before FT-003 begins.
A-05	Time Tracking uses one hourly rate per project (not per task or per role). This simplification is acceptable to the Agency Director persona for MVP.	Per-task or per-role rates required → data model revision needed; estimate increases by ~1 week.

8.2 Constraints

This process governs any addition, removal, or modification to Q2 scope from the date of this document's approval.

ID	Type	Constraint
CN-01	Resource	Maximum 4 developers in Q2. No confirmed budget for external contractors (Open Question Q-04 unresolved).
CN-02	Timeline	Q2 closes 13 June 2025. Features not delivered by this date do not count toward Q2 MRR contribution for board reporting.
CN-03	Technical	All Q2 features must work on the existing TaskFlow web platform. Mobile-specific implementations are out of scope.
CN-04	Data / Regulatory	Time Tracking billing data must not be accessible across competing client accounts. Data isolation enforced by FT-007 (Refactor) is a hard requirement.
CN-05	Process	Scope additions require formal written change request reviewed by BA, estimated by SH-03, and approved by SH-01 before any work begins.

9. Scope Change Control Process

This process governs any addition, removal, or modification to Q2 scope from the date of this document's approval.

Step	Action	Owner	Timeframe
1	Stakeholder submits written scope change request to BA (email or document comment). Must state: what change, why, and which OKR it serves.	Any stakeholder	Before raising in any meeting
2	BA analyses impact: which in-scope features are displaced, delayed, or descoped. Documents the trade-off.	BA (Duy Thien)	Within 2 business days
3	Tech Lead provides revised estimate and confirms dependency changes.	SH-03 (Bao Trung)	Within 2 business days of BA analysis
4	CEO reviews trade-off and makes final approval decision in writing.	SH-01 (Minh Khoa)	Within 1 business day of Tech estimate
5	BA updates Scope Document (version increment) and notifies all stakeholders.	BA (Duy Thien)	Within 1 business day of approval

10. Open Questions (Scope-Blocking)

These must be resolved before associated sprint planning can be finalised. Unresolved items block sprint kickoff for affected features.

ID	Question	Feature Blocked	Owner	Deadline
Q-01	Mobile App: Native iOS/Android vs React Native? Affects whether Q2 UX research can begin concretely.	FT-004 Q3 prep	SH-03	17/03/2025
Q-02	Export Excel MVP scope: 3 view types or all 12? — Highest-priority open question. Determines FT-001 estimate (3 wks vs 7–8 wks).	FT-001: Export Excel	SH-02 + SH-04 + SH-03	17/03/2025
Q-03	Refactor risk quantification: probability and cost of permission-related bugs per sprint if Q2 proceeded without refactor. Required only if scope is reconsidered.	FT-007 justification	SH-03	17/03/2025
Q-04	Is there Q2 budget for a temporary external developer to support Mobile App architecture planning while core team focuses on in-scope features?	FT-004 Q3 prep	SH-01	17/03/2025
Q-05	Public API: What external systems do the 3 enterprise prospects need to integrate with? Affects API schema complexity for Q3 planning.	FT-005 Q3 scope	SH-02	17/03/2025

11. Sign-off

Once signed, this Scope Document becomes the Q2 baseline. Changes must follow the process in Section 9. The BA then proceeds to Step 06: BA Delivery Plan.

Role	Name	Date Reviewd	Decision
CEO / Co-founder	Minh Khoa (SH-01)		
Head of Sales	Thu Hang (SH-02)		
Tech Lead	Bao Trung (SH-03)		
Customer Success Manager	Linh Phuong (SH-04)		
