
Stakeholder Analysis & Matrix

for

**<TaskFlow Q2/2025 — Work
Management Platform>**

Version 1.0 – Draft

Prepared by Duy Thien

Personal Project

Date: Apr 2026

Table of Contents

- 1. Executive Summary1
- 2. Power / Interest Grid.....2
- 3. Detailed Stakeholder Profiles.....3
 - 3.1 SH-01 — Minh Khoa (CEO / Co-founder) 3
 - 3.2 SH-02 — Thu Hang (Head of Sales) 4
 - 3.3 SH-03 — Bao Trung (Tech Lead) 5
 - 3.4 SH-04 — Linh Phuong (Customer Success Manager) 6
 - 3.5 SH-05 — Agency Director (External User Persona) 6
 - 3.6 SH-06 — Project Manager / Team Lead (External User Persona) 7
- 4. RACI Matrix8
- 5. Communication Plan.....9
- 6. Stakeholder Risk Assessment.....10
- 7. Attitude Shift Plan.....11
- 8. Open Questions — Stakeholder-Originated.....14
- Sign-off15


Revision History

Name	Date	Reason For Changes	Version

1. Executive Summary

Total Stakeholders Identified	6 stakeholders across 4 functions (Executive, Sales, Engineering, Customer Success) + 2 external user personas
Key Decision Makers	Minh Khoa (SH-01) — CEO; Thu Hang (SH-02) — Head of Sales
Highest Risk Stakeholder	SH-02 — Thu Hang (Head of Sales) — High power + active pressure to prioritise Export Excel and Time Tracking ahead of tech recommendations; disagreement with SH-03 on delivery sequence is a live conflict risk
Critical Action	Facilitate a conflict resolution session between SH-02 and SH-03 before Sprint 1 kickoff (target: 17 March 2025) to align on the final delivery sequence and avoid disruption to BA requirements delivery
Workflow Step	Step 03 — Stakeholder Analysis (prerequisite for Step 04 Business Case and all elicitation sessions)

2. Power / Interest Grid

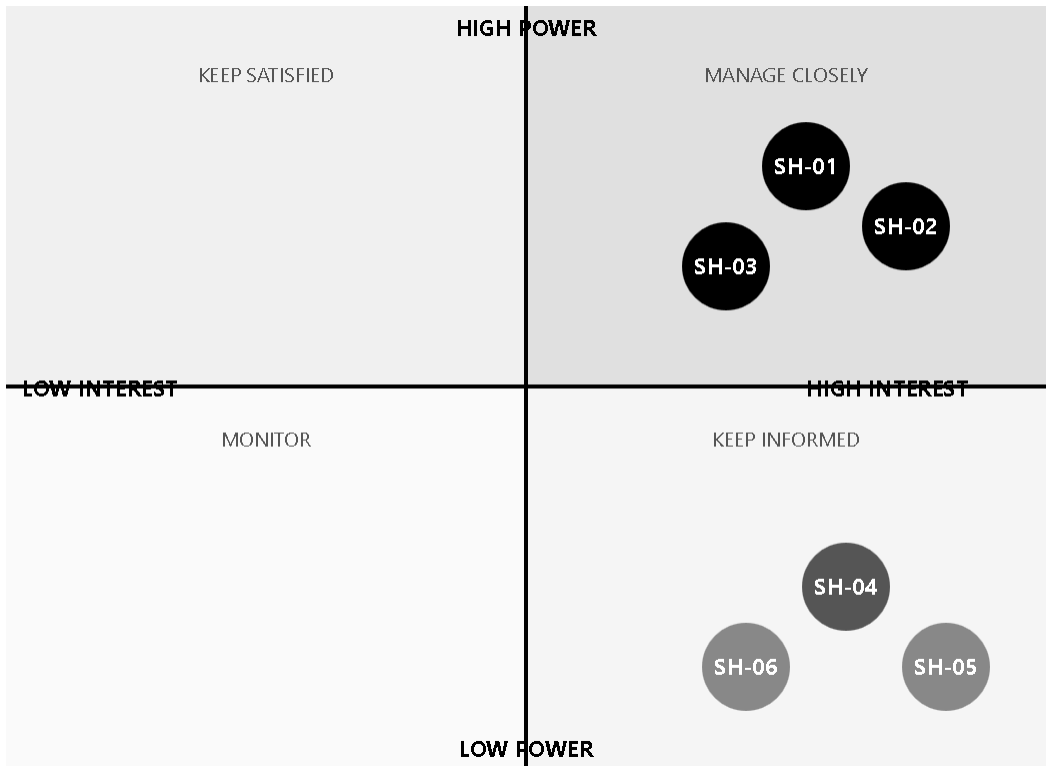

Stakeholders are plotted on the Power / Interest matrix to determine the appropriate engagement strategy for each.

Quadrant	Stakeholders	Strategy
Manage Closely (High Power, High Interest)	SH-01, SH-02, SH-03	Active engagement — weekly status updates, direct involvement in BRD review, facilitated conflict resolution between SH-02 and SH-03
Keep Satisfied (High Power, Low Interest)	—	N/A for this project
Keep Informed (Low Power, High Interest)	SH-04, SH-05, SH-06	Regular communication — sprint demos, pilot program involvement, feedback sessions; SH-04 is internal proxy for SH-05 & SH-06 voices
Monitor (Low Power, Low Interest)	—	N/A for this project

3. Detailed Stakeholder Profiles

Each stakeholder is profiled with attributes drawn from the BA skill stakeholder-map framework: attitude, concerns, win condition, and engagement strategy.

3.1 SH-01 — Minh Khoa (CEO / Co-founder)

Power Level	HIGH — Final approval authority on all Q2 scope, budget, and BRD sign-off
Interest Level	HIGH — Q2 delivery directly impacts Series A metrics (churn <3%, MRR 600M VND)
Current Attitude	Champion — Actively driving Q2 initiative; frustrated by current 5.2% churn
Desired Attitude	Champion — Maintain and strengthen; convert frustration into systematic delivery tracking
Key Concerns	Speed to market (Q2 deadline is non-negotiable for Series A credibility); stakeholder conflicts delaying BA; risk of over-scoping
What They Value	Data-driven decisions; clear ROI per feature; delivery predictability; board-presentable metrics
Influence On	All internal stakeholders — final escalation authority; influences investor confidence externally
Win Condition	Q2 delivers 5 features on schedule → churn drops below 3% → MRR reaches 600M VND → Series A narrative is credible by Q4/2025
Engagement Strategy	Weekly BA progress email; BRD review in Week 1 Sprint 0; visible OKR-to-feature traceability in all BA documents; escalate SH-02/SH-03 conflict for CEO ruling by 17/03

3.2 SH-02 — Thu Hang (Head of Sales)

Power Level	HIGH — Controls sales pipeline, prospect relationships, and revenue forecasts; directly influences CEO decisions via commercial data
Interest Level	HIGH — 180M VND/year in blocked deals depend on Export and Time Tracking; compensation likely tied to MRR growth
Current Attitude	Champion (commercially) / Pressure-driver — Pushing hard for Export Excel and Time Tracking delivery first; in conflict with SH-03 on delivery sequence
Desired Attitude	Champion + Collaborative — Aligned with Engineering on delivery sequence; trusts the phased plan delivers commercial outcomes on time
Key Concerns	Losing the 3 at-risk accounts; not closing the 180M VND blocked pipeline before competitors act; Refactor being prioritised over customer-visible features
What They Value	Revenue impact per feature; prospect conversion data; competitive differentiation; fast delivery of customer-visible features
Influence On	SH-01 (CEO) — Sales data shapes budget and priority decisions; external prospects and at-risk account retention
Win Condition	Export Excel and Time Tracking in customers' hands before Q2 ends → at least 2 blocked deals close → at-risk accounts retained → MRR target met
Engagement Strategy	Share Export MVP decision rationale in writing with committed Q3 roadmap for remaining view types; include SH-02 in facilitated SH-02/SH-03 conflict session; send bi-weekly feature delivery milestone updates; involve in FT-001 and FT-002 elicitation sessions

3.3 SH-03 — Bao Trung (Tech Lead)

Power Level	HIGH — Controls engineering capacity, sprint planning, and technical feasibility assessments; gatekeeper for what can realistically be delivered
Interest Level	HIGH — Directly accountable for Q2 engineering delivery; motivated to fix Permission Module tech debt that is currently causing 30–40% overhead per feature
Current Attitude	Supporter — Technically engaged and competent; frustrated by sales pressure to skip Refactor and build on unstable foundations; concerned about over-promising to customers
Desired Attitude	Champion — Empowered to lead Sprint 1 Refactor with full stakeholder backing; trusted partner in scoping what's feasible
Key Concerns	Building FT-002/FT-003/FT-006 on top of broken permission architecture → post-launch bugs; unrealistic timelines set by Sales without engineering input; Q-02 (Export scope) ambiguity delaying planning
What They Value	Technical correctness; realistic scoping; internal documentation quality; BA deliverables that are dev-ready (testable, traceable requirements)
Influence On	4 junior/senior developers — sets engineering culture; SH-01 (CEO) on technical risk assessment
Win Condition	Permission Refactor approved as Sprint 1 with full stakeholder buy-in → all 5 Q2 features delivered without critical permission bugs → tech debt eliminated entering Q3
Engagement Strategy	Include in BA delivery plan as co-author of technical estimates; share BRD review access with 5-day turnaround SLA; conduct 1-day refactor discovery session before Sprint 1; facilitate Sprint 0 conflict resolution with SH-02

3.4 SH-04 — Linh Phuong (Customer Success Manager)

Power Level	LOW — No direct authority over scope or budget decisions
Interest Level	HIGH — Manages 89 support tickets/quarter; directly faces customer complaints from missing Notification, Export, and Time Tracking features
Current Attitude	Supporter — Actively engaged; brings real customer voice into planning; wants features deployed that will reduce daily support burden
Desired Attitude	Champion — Recruited as pilot program owner; invested in successful feature adoption
Key Concerns	At-risk accounts churning before features ship; customers misunderstanding MVP scope; no dedicated QA for UAT meaning issues reach customers
What They Value	Customer satisfaction; reduction in reactive support volume; proactive communication to at-risk accounts; onboarding materials for new features
Influence On	SH-01 via churn and NPS data; external customers and at-risk accounts (SH-05, SH-06 personas)
Win Condition	Notification and Export features deployed → top 3 support ticket categories resolved → pilot customers successfully adopt Time Tracking → NPS rises above 40
Engagement Strategy	Assign as pilot customer recruitment lead for FT-002 beta; include in elicitation for FT-001, FT-003; provide advance feature preview with onboarding guide draft; bi-weekly check-in during Q2

3.5 SH-05 — Agency Director (External User Persona)

Power Level	LOW — No internal decision authority; influence via churn threat and sales pipeline
--------------------	--

Interest Level	HIGH — Needs Time Tracking + Export Excel for billable hours reporting to clients; currently using Toggl + manual Excel reconciliation
Current Attitude	Neutral / At-risk — Using TaskFlow for task management but evaluating Monday.com due to missing billing and reporting features
Desired Attitude	Supporter → eventual Champion; retained and upgraded to Enterprise plan via Time Tracking adoption
Key Concerns	Billing accuracy for client invoices; agency profitability dependent on accurate hour tracking; whether TaskFlow will match competitor features in time
What They Value	Single system for task + time + billing; professional client-ready PDF/Excel exports; data reliability; no manual reconciliation
Influence On	Purchase decisions for 5–20 seat Agency accounts; referrals to other agency owners in their network
Win Condition	Time Tracking + Export Excel available by end of Q2 → replaces Toggl → client invoicing done from TaskFlow → continues subscription and upgrades to Enterprise
Engagement Strategy	Represented by SH-04 (CSM) in stakeholder sessions; recruit 2–3 Agency Directors as pilot customers for FT-002 beta; CSM conducts QBR during Q2 to communicate Q2 roadmap commitment

3.6 SH-06 — Project Manager / Team Lead (External User Persona)

Power Level	LOW — Influencer within their team; adoption driver for TaskFlow platform
Interest Level	HIGH — Primary daily user of TaskFlow; needs Bulk Action and Notification to reduce manual status management overhead
Current Attitude	Supporter — Using TaskFlow daily but relies on Zalo for status updates and performs individual task edits at sprint-end (15–20 mins per sprint)

Desired Attitude	Champion — Satisfied power user who recommends TaskFlow internally and in their professional network
Key Concerns	Notification reliability (missing overdue alerts); sprint-end status update effort; team confusion from duplicate Zalo + TaskFlow communication
What They Value	Speed and efficiency; reduce duplicate communication channels; clear task ownership and accountability; mobile-accessible (future Q3)
Influence On	Team Members' daily usage patterns; Team Member adoption/abandonment of the platform
Win Condition	Notification System eliminates Zalo dependency → Bulk Action reduces sprint-end work to under 2 minutes → team fully migrated to TaskFlow as single source of truth
Engagement Strategy	Include 2–3 PMs in FT-003 and FT-006 elicitation sessions; recruit for UAT; SH-04 collects NPS data post-Q2 launch

4. RACI Matrix

Defines roles for each BA and project activity. One Accountable (A) per activity. At least one Responsible (R) per activity. C = Consulted, I = Informed.

BA / Project Activity	SH-01 CEO	SH-02 Sales	SH-03 Tech Lead	SH-04 CSM	BA Duy Anh
Q2 Scope Approval	A	C	C	I	R
BRD Review & Sign-off (DOC-05)	A	C	C	I	R
Stakeholder Elicitation Interviews	I	C	C	C	A / R
Feature Requirements Definition (Use Cases, User Stories)	I	C	C	C	A / R
Priority Conflict Resolution (SH-02 vs SH-03)	A	R	R	I	C

BA Delivery Plan & Timeline (DOC-04)	I	I	C	I	A / R
Open Question Resolution (Q-01 to Q-04)	A	R	R	C	C
Sprint Planning & Capacity Confirmation	I	I	A / R	I	C
Pilot Customer Recruitment (FT-002 Beta)	I	C	I	A / R	C
UAT Facilitation & Sign-off	A	I	C	R	R
Post-Launch Metric Review (QA-01 to QA-08)	A	I	I	R	C

Legend: R = Responsible (does the work) · A = Accountable (owns the outcome) · C = Consulted (input required) · I = Informed (kept updated). Exactly one A per row.

5. Communication Plan

Tailored communication strategy for each stakeholder group, specifying method, frequency, content, owner, and feedback channel.

Stakeholder Group	Method	Frequency	Content	Owner	Feedback Channel
Key Players SH-01, SH-02, SH-03	1:1 meeting or shared Slack channel	Weekly (Monday)	BA deliverables status, open questions log, decisions needed, risk flags	BA (Duy Anh)	Direct reply / Slack thread
BRD Sign-off Cycle SH-01, SH-02, SH-03	Email with document attachment	Per document release (5-day SLA)	BA deliverable (BRD, Use Cases, User Stories) with review checklist and decision deadline	BA	Email reply or Google Doc comments
Keep Informed SH-04	Bi-weekly Slack update + monthly demo	Bi-weekly	Feature delivery progress, pilot program preparation, customer feedback integration	BA / PM	Slack / Google Meet

External Users SH-05, SH-06 (via SH-04)	Pilot program invitations, QBR, CSM outreach	Monthly during Q2	Q2 roadmap commitments; beta testing invitation; onboarding guides post-launch	SH-04 (CSM)	Customer feedback form / CSM note
Conflict Resolution SH-02 + SH-03	Facilitated session (BA-led, CEO moderates)	Once — target 17 March 2025	Delivery sequence rationale (Refactor first), Export scope decision (3 vs 12 views), Q2 timeline impact assessment	BA + SH-01	Written decision document distributed within 24hrs
All Stakeholders	Sprint Review Demo (video or live)	Every 2 weeks (end of sprint)	Working feature demo, velocity data, next sprint goals, open risks	SH-03 (TL) + BA	Sprint retrospective + async Slack Q&A

6. Stakeholder Risk Assessment

Risk ID	Risk Description	Stakeholder	Probability	Impact	Mitigation
SR-01	SH-02 (Sales) escalates Export scope conflict directly to CEO, bypassing BA facilitation, causing scope change after BRD is signed	SH-02	Medium	Critical	Conduct conflict resolution session before BRD finalisation (17/03); CEO (SH-01) makes binding scope ruling in writing; BA documents immediately
SR-02	SH-03 (Tech Lead) underestimates Refactor complexity during discovery, causing Sprint	SH-03	Medium	Critical	Schedule 1-day tech spike before Sprint 1; hard-cap Refactor scope to 5 fixed roles only; any

	1 to overrun and delaying all downstream features				additional work is a formal scope change request
SR-03	SH-04 (CSM) is unable to recruit minimum 3 active pilot customers for FT-002 beta, causing Time Tracking to launch without validated real-world usage data	SH-04	Low	High	Pilot recruitment begins in Week 2 with incentive (early access + priority support); minimum 3 active users required before general release is approved by SH-01
SR-04	SH-01 (CEO) deprioritises BA deliverable reviews due to investor/fundraising demands, causing sign-off delays that push sprint kickoffs	SH-01	Low	Critical	Async written review accepted as alternative to live sessions; 5-day review SLA agreed upfront; SH-01 can delegate to SH-03 for technical sections
SR-05	External customers (SH-05 persona) churn before Q2 features ship because a competitor announces Vietnamese-language support or significant pricing changes	SH-05	Low	Critical	SH-04 schedules QBR with all 3 at-risk accounts in April; communicates Q2 roadmap as a committed delivery; CSM offers interim reconciliation support where possible

7. Attitude Shift Plan

Documents the desired attitude shift for each stakeholder requiring engagement effort, and the specific actions to achieve that shift.

Stakeholder	Current Attitude	Target Attitude	Gap	Actions to Shift	Target Date
SH-02 — Thu Hang	Champion (commercially) + Pressure-driver — In conflict with SH-03; pushing to skip Refactor	Champion + Collaborative — Aligned with Engineering on phased delivery sequence	Needs to understand why Refactor-first is a lower-risk path to her commercial goals, not a delay	1. Facilitated session showing: "Refactor-first = fewer bugs in FT-001/FT-002 = faster to customer hands" · 2. Share BA Delivery Plan timeline showing Export and Time Tracking landed by Wk 8 even with Refactor-first · 3. Committed Q3 roadmap for remaining 9 Export view types in writing	17/03/2025
SH-03 — Bao Trung	Supporter — Technically engaged but feeling unheard by Sales stakeholders; concerned about overcommitment	Champion — Empowered technical leader with full stakeholder backing for Sprint 1 Refactor direction	Needs formal backing from SH-01 and documented acknowledgment that Refactor is a technical necessity, not optional	1. CEO ruling in conflict resolution session that Refactor is Sprint 1 (non-negotiable) · 2. BA documents Refactor rationale in Scope Document (DOC-03) with explicit	17/03/2025

				link to feature delivery risk · 3. Include SH-03 as co-author of technical effort estimates in BRD	
SH-04 — Linh Phuong	Supporter — Engaged but lacks formal ownership of any Q2 workstream	Champion — Invested owner of pilot program and post-launch adoption measurement	Needs formal role assignment and recognition that her customer proximity makes her critical to Q2 success	1. Formally assign SH-04 as Pilot Program Lead in BA Delivery Plan RACI · 2. Include SH-04 in elicitation sessions for FT-001, FT-002, FT-003 · 3. Share post-launch metric ownership (NPS, ticket volume reduction) with SH-04	24/03/2025
SH-05 — Agency Director	Neutral / At-risk — Evaluating Monday.com alternatives due to missing billing and reporting features	Supporter — Retained and confident TaskFlow will fit their agency workflow by end of Q2	Needs credible commitment evidence that Time Tracking and Export will ship in Q2, not vague "coming soon" messaging	1. SH-04 communicates Q2 roadmap with milestone dates during QBR · 2. Invite to FT-002 beta pilot program with direct access to new feature	30/04/2025

				pre-launch · 3. CSM follows up with personalised onboarding support at launch	
--	--	--	--	---	--

8. Open Questions — Stakeholder-Originated

ID	Question	Raised by	Assigned To	Target Date	Status
Q-01	Should Mobile App (FT-004) be reconsidered for Q2 given 4 churned customers cited it as the primary reason?	SH-02 (Sales)	SH-01 (CEO)	17/03/2025	Open
Q-02	Is the Export Excel MVP scope confirmed as 3 view types only, or does the sales pipeline minimum require more?	SH-02 (Sales)	SH-01 to rule; SH-03 to assess	17/03/2025	CRITICAL — Blocks FT-001 BRD
Q-03	Can the engineering team realistically deliver all 5 Q2 features with 4 developers in 11 weeks?	SH-03 (Tech Lead)	SH-01 + SH-03	17/03/2025	Open
Q-04	Is there budget to engage an external designer and QA engineer to support Q2 delivery?	BA	SH-01 (CEO)	17/03/2025	Open

Sign-off

Signature below confirms that this Stakeholder Analysis accurately represents the identified stakeholders and authorizes the BA to proceed to Stakeholder Elicitation and Step 04 Business Case.

Role	Name	Date Reviewd	Signature
CEO / Sponsor	Minh Khoa (SH-01)		
Head of Sales	Thu Hang (SH-02)		
Tech Lead	Bao Trung (SH-03)		
